



Public Building Commission of Chicago

Board Meeting
January 14, 2014





Board Meeting
January 14, 2014

Awards



Board Meeting
January 14, 2014

2013 American Society of Heating, Refrigerating and Air-Conditioning Engineers (ASHRAE)

Award of Engineering Excellence for its superior and
sustainable engineering systems design.

Sarah E. Goode STEM Academy on December 12, 2013





Board Meeting
January 14, 2014

Completed Projects



Hale Elementary School Linked Annex


6140 S. Melvina Avenue: Ward 23

Board Meeting
January 14, 2014



Project Features

- Three-story addition
- 41,338 Square Feet
- Kitchen and Dining Facility
- 11 Classrooms
- 1 Computer Lab
- 1 Art Room
- 2 Student Pull-out Rooms
- 3 Administrative Offices
- Installation of Acoustic Panels in the Auditorium

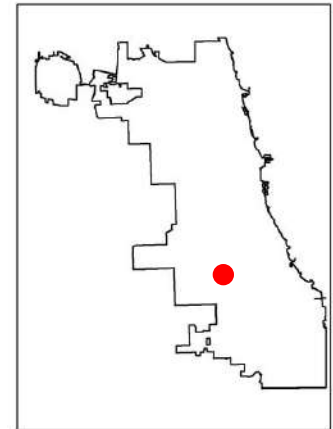



Hale Elementary School Linked Annex

6140 S. Melvina Avenue: Ward 23

Board Meeting
January 14, 2014



Budget to Actual

- Budget Authority: \$15,837,887
- Current Projection: \$14,955,703
- **Variance: (\$882,184) Under Budget**


Schedule

- **Opened: January 2014**

Economic Sustainability

- Pay App 7: (54.09%)
- MBE Paid-to-date: 20.19% or \$1,254,668
- WBE Paid-to-date: 3.18% or \$197,879
- Total Individuals Employed: 337
- Full-time Equivalent Jobs: 57
- Community Hires: 17

General Contractor: Walsh Construction Company
Architect of Record: ESA/Searl

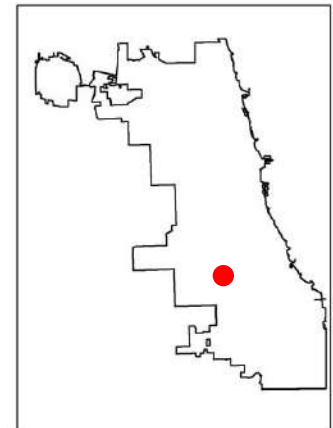



Edison Park Elementary School Linked Annex


6220 N. Olcott Avenue: Ward 41

Board Meeting
January 14, 2014



Project Features

- Two-story addition
- 30,560 Square Feet
- Kitchen and Dining Facility
- 9 Classrooms
- 1 Science Lab
- Renovation of 2 Existing Classrooms
- Playlot
- Parking lot

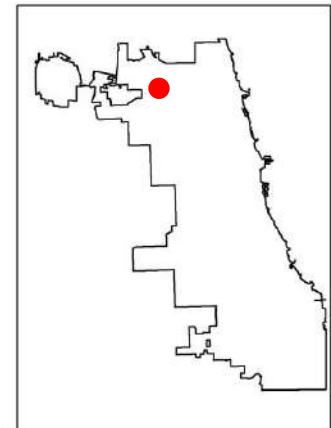



Edison Park Elementary School Linked Annex

6220 N. Olcott Avenue: Ward 41

Board Meeting
January 14, 2014



Budget to Actual

- Budget Authority: \$14,077,194
- Current Projection: \$13,215,339
- **Variance: (\$861,855) Under Budget**


Schedule

- **Opened: January 2014**

Economic Sustainability

- Pay App 6: (52.27%)
- MBE Paid-to-date: 41.19% or \$2,239,977
- WBE Paid-to-date: 3.25% or \$176,683
- Total Individuals Employed: 367
- Full-time Equivalent Jobs: 49
- Community Hires: 9

General Contractor: Walsh Construction Company
Architect of Record: Tripartite, Inc.

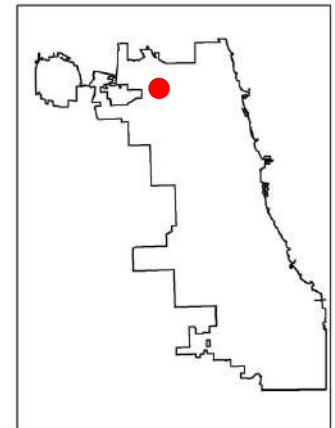



Board Meeting
January 14, 2014

Forecast 2014: Projects in Development



Board Meeting
January 14, 2014

Chicago Children's Advocacy Center City of Chicago



Board Meeting
January 14, 2014

Chicago Children's Advocacy Center

1240 S. Damen Avenue: Ward 2



Project Features

- 27 Offices (Exec. Admin and States Attorney)
- 33 Workstations
- 10 Mental Health Offices/Therapy Rooms
- 5 Therapy Rooms
- Lunch Room/Breakout Space
- Multipurpose Room/Training Center
- Forensic Interview Rooms Renovation
- Family Room Area Renovation


Budget to Actual

- Budget Authority: \$9,000,000
- Current Projection: \$9,000,000
- **Variance: \$0 On Budget**

General Contractor: IHC Construction
Architect of Record: Holabird & Root

Schedule

- General Contractor awarded 10/1/13. In process with submittals, pre-construction documents, shop drawings and permitting.
- Groundbreaking ceremony targeted for: **March 2014**
- Projected Substantial Completion: November 2014
- Projected Facility Opening: **December 2014**

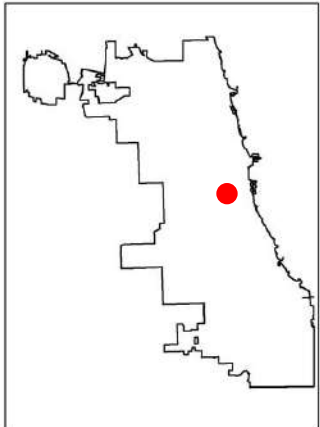



Board Meeting
January 14, 2014

Chicago Public Library



Board Meeting
January 14, 2014

Whitney Young Branch Library

7901 Dr. Martin Luther King Jr. Drive: Ward 6



Budget to Actual:

Land, Remediation and Planning

- Budget Authority: \$4,559,925
- Current Projection: \$4,559,925
- **Variance: \$0 On Budget**

Formulation Services


- Formulation 8/20/2013
- Land acquisition, environmental remediation, building assessment, concept design, and site conditions due diligence

Project Features

- Environmental remediation and planning activities for a new addition project.

Schedule

- Remediation complete 12/2013
- Existing building system assessment complete
- Program and concept design for addition in development
- Design & Construction: Pending program and budget confirmation

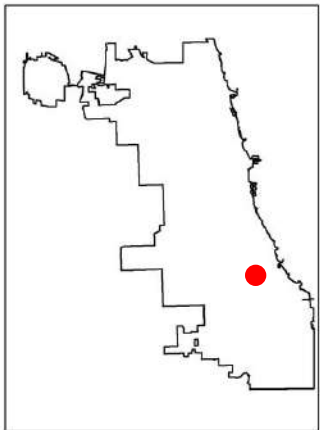



Board Meeting
January 14, 2014

Chinatown Branch Library

2121 S. Archer Avenue: Ward 25



Project Features

- Approximately 16,000 Square Feet
- Two story steel framed building
- Large reading room
- Media room
- Juvenile/children's reading room
- Flexible meeting spaces for community use


Schedule

- Projected Facility Opening:
February/March 2015 (Pending Land)

Design Builder: Wight & Company

Budget to Actual

- Land
 - 2 properties in condemnation
- Vertical Construction
 - Vertical Construction
Budget Authority: \$12,000,000
 - Current Vertical
Construction Projection: \$12,000,000
 - Vertical Construction
Variance: \$0 On Budget

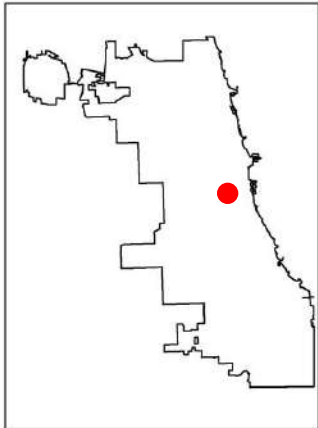



Board Meeting
January 14, 2014

Albany Park Branch Library

5150 N. Kimball Avenue: Ward 39



Project Features

- 16,300 Square Feet
- On-site parking for 16 vehicles (including handicapped accessible)
- Attractive landscaping with a generous Reading Garden planned on the west side of the new library
- Reading Room
- New opening day collection and increased capacity
- Multipurpose Room
- Teen space with technology workshops
- 38 Public Computers
- Laptop computer connections at study tables


Schedule

- 29% Complete
- Projected Substantial Completion: May 2014
- Projected Facility Opening: **August 2014** (allowing time for CPL move-in)

Budget to Actual

- Budget Authority: \$14,773,728
- Current Projection: \$14,425,569
- **Variance: (\$348,159) Under Budget**

General Contractor: Wight Construction
Architect of Record: Jackson Harlan

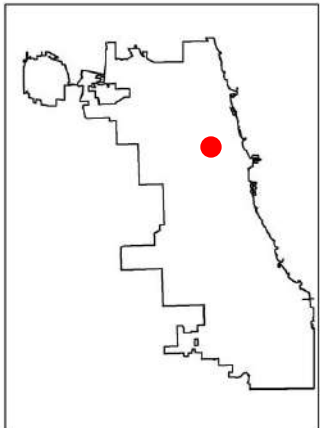



Board Meeting
January 14, 2014

Chicago Public Schools




Board Meeting
January 14, 2014

Southeast Area Elementary School

104th Street and Indianapolis Avenue Ward: 10



V:\99 CW\05 Chicago Public Schools\05310 Southeast Area ES\04 Planning and Design\04 Land\03 Property Acquisition\AER_PBC_KRS_SEAES\04R\LRUNK\TADC_2012\13

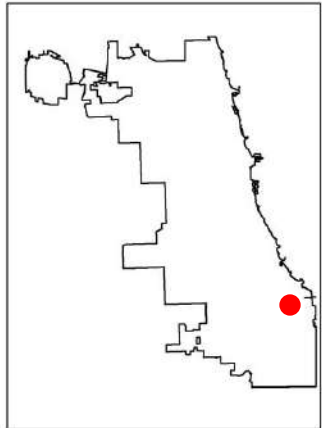

Schedule

- Undertaking 11/12/2013
- Land acquisition complete
- Concept design in development
- **Anticipated school facility opening Fall 2016**




Board Meeting
January 14, 2014

Southwest Area Elementary School

West 60th Street and South Karlov Avenue: Ward 13



05710 4-04-01 AER_PBC_CRM_WildwoodES_20131016

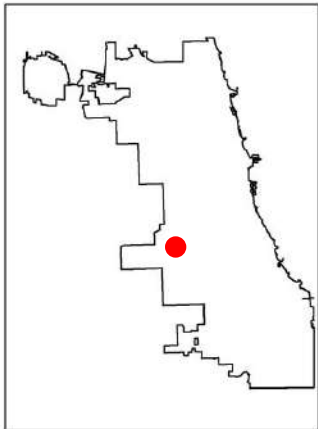

Schedule


- Formulation 12/10/2013
- Land acquisition: CPS owned
- **Anticipated school facility opening Fall 2016**



Board Meeting
January 14, 2014

Oriole Park Elementary School Annex

5424 N. Oketo Avenue: Ward 41

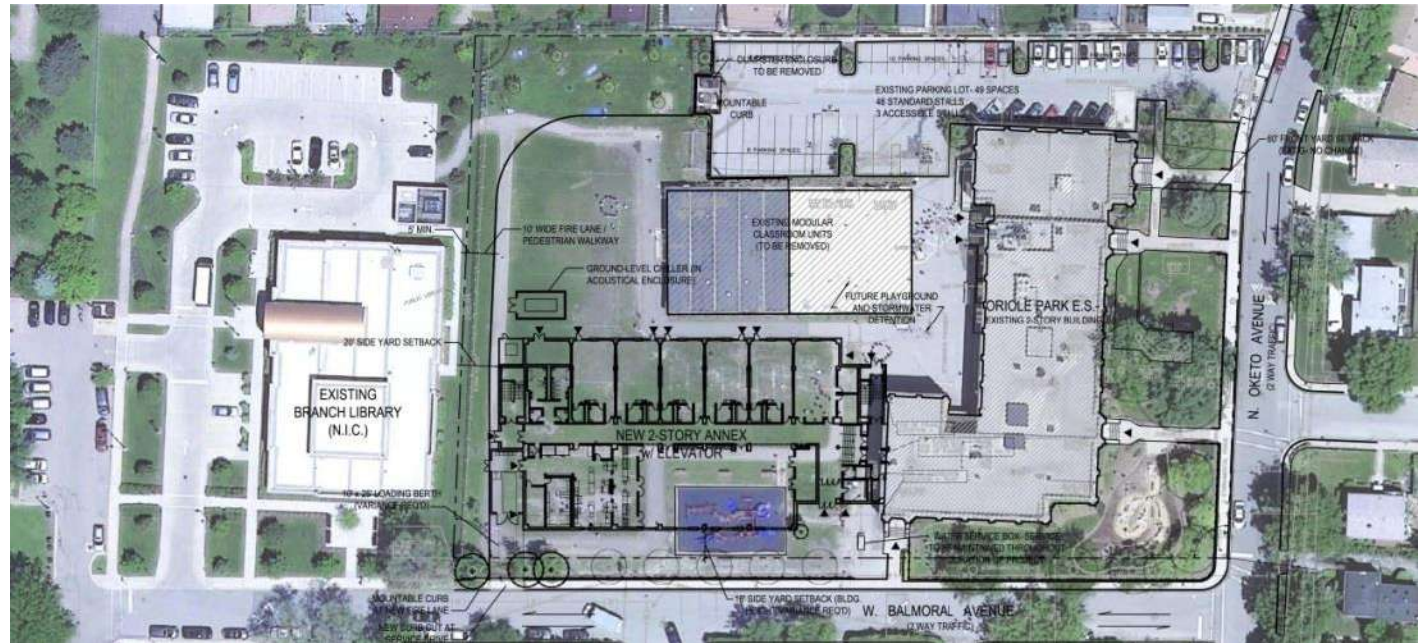

Project Features

- 17 classrooms
- 2 administrative offices
- Library/Media Resource Center
- Kitchen and dining center
- Minor existing building renovations
- Site development includes modular removal and new playground


Budget to Actual

- The \$4M partial undertaking for planning and design has been authorized by CPS
- Full undertaking 11/12/2013
- Budget proposal in development

Architect of Record: Wallin Gomez Architects, Ltd.

Schedule

- Conceptual programming and cost estimating are complete
- Design phase underway
- **Anticipated school facility opening August 2015**

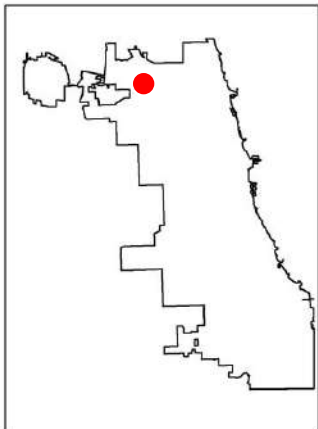



Board Meeting
January 14, 2014

Wildwood Elementary School Annex

6950 N. Hiawatha Avenue: Ward 41



Project Features

- 14 classrooms
- Library/media resource center
- Administration office
- Kitchen
- Minor existing building renovations
- Site development features include basketball, parking and modular removal


Budget to Actual

- The \$3.25M partial undertaking for planning and design has been authorized by CPS
- Full undertaking 11/12/2013
- Budget proposal in development

Architect of Record: Ilekis Associates

Schedule

- Conceptual programing and cost estimating in process
- **Anticipated school facility opening August 2015**

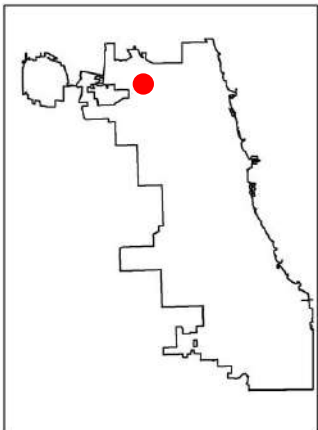




Board Meeting
January 14, 2014

Walter Payton College Preparatory High School Addition

1034 N. Wells Street: Ward 27

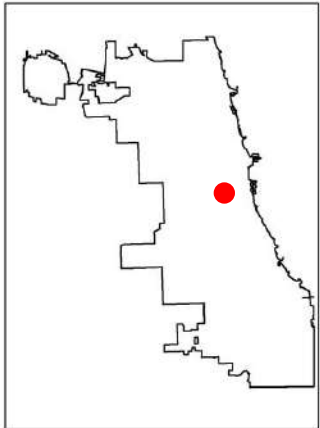

Project Features

- 14 classrooms
- Administrative office
- Gymnasium and shower/locker facilities
- Physical education and fitness rooms
- Café
- Minor existing building renovations
- Site development

Schedule

- Concept options complete
- Preliminary Environmental analysis of site complete
- Preliminary Geo-Tech tests complete
- **Anticipated school facility opening TBD December 2015.**

Budget to Actual

- The \$3.75M partial undertaking for planning and design has been authorized by CPS.
- Full undertaking 11/12/2013
- Budget proposal in development

Architect of Record: Koo and Associates



Board Meeting
January 14, 2014

Abraham Lincoln Elementary School Annex

615 W. Kemper Place: Ward 43



Project Features

- 19 classrooms
- Dining center
- Hybrid Kitchen
- Rooftop playlot
- Minor existing building renovations
- Site development
- Playlot


Budget to Actual

- The \$4.6M partial undertaking for planning and design has been authorized by CPS.
- Partial undertaking 12/10/2013
- Budget proposal in development

Architect of Record: Muller + Muller

Schedule

- Environmental and geotechnical testing is underway
- Program and test fit are in development
- **Anticipated school facility opening TBD**

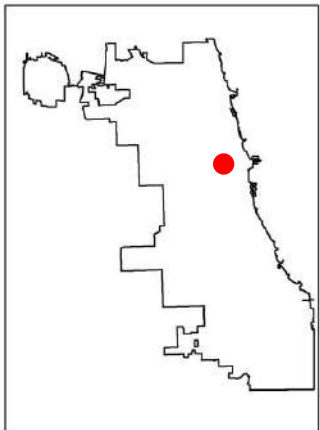




Board Meeting
January 14, 2014

Turf Field at NTA

23rd & Dearborn: Ward 3

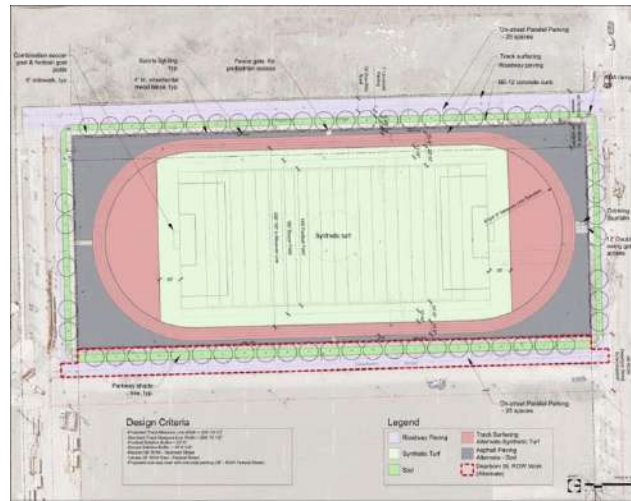

Project Features

- Artificial turf field (high school-standard football and soccer practice field)
- Four lane polyurethane running track (400M non-standard track)
- Long jump, high jump, pole vault infrastructure
- Sports lighting
- Ornamental Fencing
- 50 parallel parking spaces


Schedule

- Schedule pending land transfer

Budget to Actual

- Budget Authority: \$5,600,000
- Current Projection: \$5,600,000
- **Variance: \$0 On Budget**
- DPD to confirm funding available for project

Architect of Record: Hitchcock Design Group

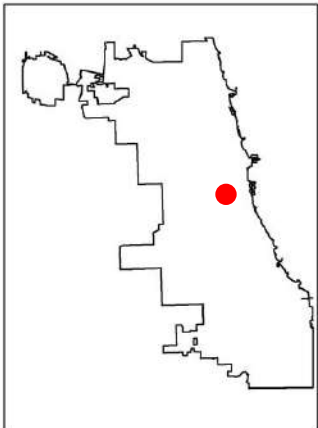





Chicago Vocational Career Academy

2100 E. 87th Street: Ward 8


Board Meeting

January 14, 2014

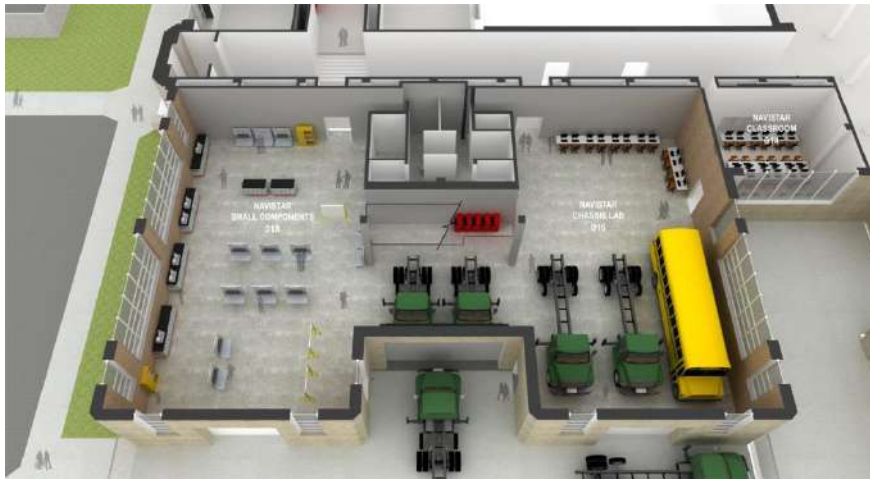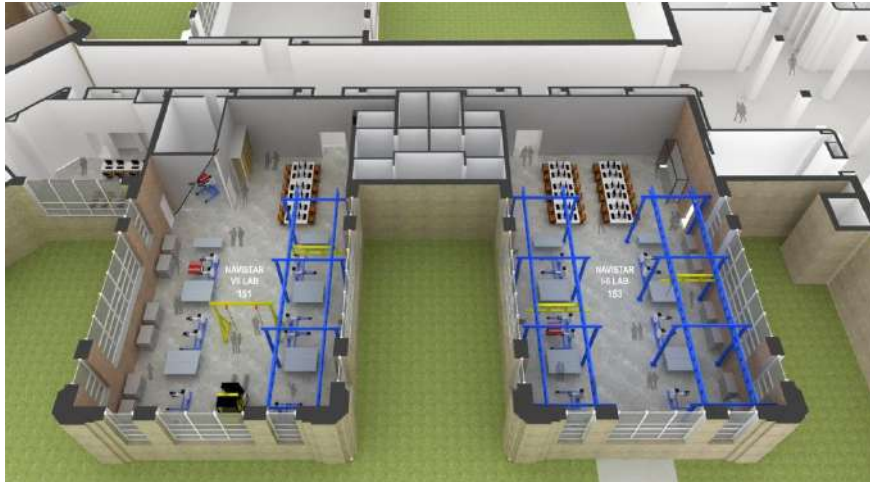

Project Features

- Interior program renovations and upgrades:
- Career and technical education spaces
- Early College Science, Technology, Engineering and Mathematics (STEM) classrooms
- Science labs
- Demolition of the Anthony Wing
- Roof replacement
- Right of way improvements
- Electrical, mechanical and plumbing upgrades
- Accessibility improvements
- Exterior envelope, structural and basement repairs

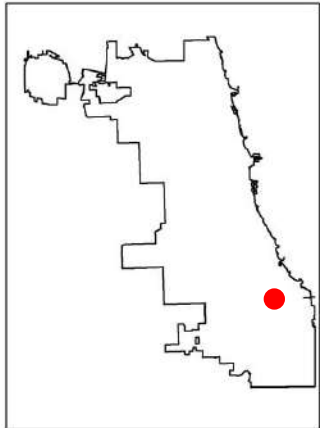




Chicago Vocational Career Academy

2100 E. 87th Street: Ward 8

Board Meeting

January 14, 2014

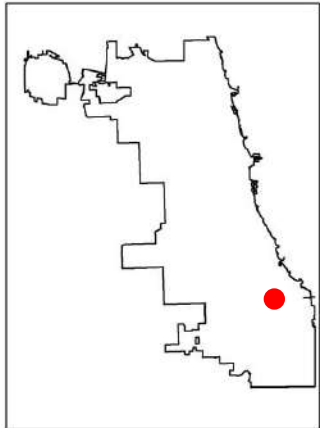

Schedule

- Outreach event held on site on November 21, 2013
- Phase I General Construction scheduled to issue for bid on **1/17/14**
- Phase I Estimated Construction from Feb 2014 to **Jan 2015**
 - Interior renovation program complete: August 2014
 - MEP and exterior complete: Mid December 2014
- Phase II Bid in Jul 2014, Estimated Construction from Aug 2014 to **Aug 2015**

Budget to Actual

- Budget Authority: \$75,000,000
- Current Projection: \$75,000,000
- **Variance: \$0 On Budget**

Architect of Record: DLR Group



Board Meeting
January 14, 2014

Coonley Elementary School Addition

4046 N. Leavitt: Ward 47



Project Features

- 12 Classrooms
- 1 Kitchen
- 1 Multipurpose Room (Dining/Assembly)
- 1 Recycling Area
- 1 Storage Room
- Interior Renovation to Select Spaces

Budget to Actual


- Budget Authority: \$16,500,000
- Current Projection: \$16,500,000

Variance: \$0 On Budget

Architect of Record:
SWWB, LTD., Architects
GC: KR Miller

Schedule

- General Contractor awarded at 12/10/13
Board Meeting
- Notice to Proceed issued to GC.
- Site preparation/caisson work in progress
for completion in January 2014.
- Projected Substantial Completion/Facility Opening:
 - **August 2014 for Building**
 - **October 2014 for Sitework**

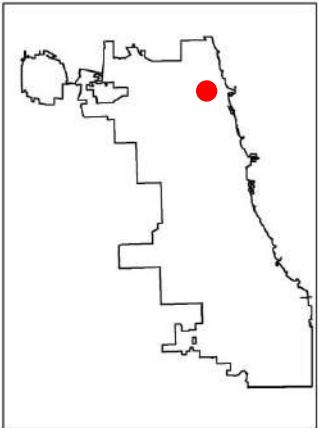



Board Meeting
January 14, 2014

Jones College Prep Renovation

606 S. State Street: Ward 2



Project Features


- Phase I: permanent canopy link to new high school, interior program renovations including pre-law lab, fitness room with locker rooms, multi purpose room, student resource center and new art rooms and exterior renovations including roof replacement.
- Phase II: Cooling plant upgrades, architectural renovations including renovation of the existing cafeteria and mechanical upgrades.

Budget to Actual

- Budget Authority: \$8,300,000
- Current Projection: \$8,300,000
- **Variance: \$0 On Budget**

Schedule

- Phase I: AOR: Perkins + Will
General Contractor: F.H. Paschen, SN Nielsen
- Phase II: AOR: Perkins + Will
General Contractor: Friedler Construction
 - 5% Complete
 - General Contractor awarded 10/1/13. Notice to Proceed issued. Demolition and Abatement work complete. Work, consisting of mechanical upgrades pending permit. To be substantially complete **March 2014**.

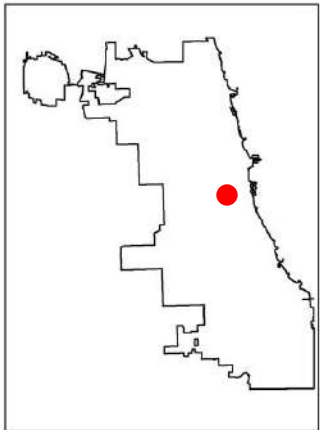



Board Meeting
January 14, 2014

Bell Elementary School Addition

3730 N. Oakley Avenue: Ward 47



Project Features

- 1 Science Lab
- 1 Art Room
- 1 Music Room
- 1 Multipurpose Cooking Kitchen
- 1 Multipurpose Room (Dining/Assembly)
- Library (Relocation and Renovation)
- Nurse's Suite (Relocation and Renovation)
- Existing Gymnasium (Floor refinishing)
- Existing Auditorium (Life safety) Upgrades
- Interior Upgrades to Select Existing Spaces

Budget to Actual

- Budget Authority: \$10,000,000
- Current Projection: \$9,409,608
- **Variance: (\$590,392) Under Budget**

General Contractor:

Wight Construction Services, Inc.

Architect of Record: SMNG-A

Schedule

- 70% Complete
- Projected Substantial Completion for New Addition:
February 2014, Spring completion for existing bldg renovation
- Projected Facility Opening for New Addition: **March 2014**
- Projected Opening for Renovation Work: June 2014

