CONTRACTOR:	
CONTACT NAME:	
ADDRESS:	
CITY/STATE/ZIP:	
PHONE NUMBER:	
FAX NUMBER:	
FMAII:	

#### TO BE EXECUTED IN DUPLICATE WHEN SUBMITTED VIA HARD COPY (BY REQUEST ONLY)

**BOOK 1:** 

# PROJECT INFORMATION, INSTRUCTIONS TO BIDDERS, AND EXECUTION DOCUMENTS

**CONTRACT NO. C1607** 

CHICAGO DEPARTMENT OF TRANSPORTATION CAPITAL PROGRAM
ALLEYS (VARIOUS LOCATIONS) – PACKAGE 1
CHICAGO, IL
PBC PROJECTS #22356A-G
CDOT PROJECT #S-3-356

# PUBLIC BUILDING COMMISSION OF CHICAGO



# Mayor Brandon Johnson Chairman

Ray Giderof Acting Executive Director

Richard J. Daley Center 50 West Washington Street Room 200 Chicago, Illinois 60602 312-744-3090

www.pbcchicago.com

ISSUED FOR BID ON: 3/28/2024

# PUBLIC BUILDING COMMISSION OF CHICAGO

# **TABLE OF CONTENTS**

I.	INTRODUCTION	2
II.	PROJECT INFORMATION	2
A.	GENERAL INFORMATION	2
B.	MANDATORY PROJECT SPECIFIC CONTRACTOR STAFFING REQUIREMENTS	3
C.	SCHEDULING SOFTWARE REQUIREMENTS	4
D.	ONLINE COLLABORATION AND DOCUMENTATION MANAGEMENT SYSTEM REQUIREMENTS	4
E.	TIME OF COMPLETION	4
F.	COMMISSION'S CONTRACT CONTINGENCY	4
G.	COPIES OF DRAWINGS AND SPECIFICATIONS	4
H.	LIQUIDATED DAMAGES	4
l.	PREVAILING WAGE RATES	5
III.	INSTRUCTIONS FOR BIDDERS	5
A.	EXAMINATION OF DOCUMENTS BY BIDDER	5
B.	INTERPRETATIONS OF ADDENDA	5
C.	PRE-QUALIFICATION OF BIDDERS	5
D.	EVIDENCE OF CONTINUING QUALIFICATIONS OF BIDDER	5
E.	PREPARATION OF BID	6
F.	BID DEPOSIT	6
G.	BIDDER'S EXECUTION OF BID	7
H.	AFFIDAVIT OF NON-COLLUSION	7
l.	MBE AND WBE COMMITMENTS	7
J.	LOCAL BUSINESS SUBCONTRACTING PARTICIPATION AND COMMUNITY HIRING	7
K.	DISCLOSURE OF RETAINED PARTIES	8
L.	SUBMISSION OF BID	8
M.	WITHDRAWAL OF BIDS BEFORE BID OPENING	8
N.	OPENING OF BIDS	8
Ο.	EVALUATION OF BIDS	8
P.	BASIS OF AWARD	8
Q.	PERFORMANCE AND PAYMENT BOND AND INSURANCE	9
R.	PROTESTS	9
S.	LICENSING	9
T.	AWARD OF CONTRACT, CANCELLATION, OR REJECTION OF BIDS	10
U.	ALTERNATES	10
IV.	BID AND EXECUTION DOCUMENTS	
A.	CONTRACTOR'S BID	11
B.	BID FORM – WPA STREET RECONSTRUCTION (FILLMORE STREET) – BASE BID	12
C.	SITE WORK ALLOWANCE SCHEDULE	13

# PUBLIC BUILDING COMMISSION OF CHICAGO

D.	SCHEDULE OF PRICES	14
E.	ADDITIONAL ALLOWANCE SCHEDULES	42
F.	ALTERNATES	42
G.	ACCEPTANCE OF THE BID	43
٧.	BID SUPPORT DOCUMENTS	44
A.	BASIS OF AWARD (AWARD CRITERIA FIGURE)	44
VI.	ADDITIONAL DOCUMENTS TO BE EXECUTED	48
	Affidavit of Non-collusion	48
	SCHEDULE B - Joint Venture Affidavit (1 of 3)	49
	SCHEDULE C - Letter of Intent from MBE/WBE (1 of 2)	52
	SCHEDULE E - Request for Waiver from MBE/WBE Participation	56
	Disclosure of Retained Parties	57
	Performance and Payment Bond	59
	Bond Approval	62
DOC	CUMENT SUBMITTAL CHECKLIST	63
EXH	IBIT #1 COOK COUNTY PREVAILING WAGE RATES – EFFECTIVE OCTOBER 5, 2023	64
EXH	IBIT #2 INSURANCE REQUIREMENTS	65
EXH	IBIT #3 PROJECT COMMUNITY AREA MAP	69
EXH	IBIT #4 ASSIST AGENCIES	70

#### PUBLIC BUILDING COMMISSION OF CHICAGO

#### I. INTRODUCTION

Thank you for your interest in bidding on this project, which is being undertaken by the Public Building Commission of Chicago. The Public Building Commission of Chicago (hereafter, the PBC, or Commission) is a municipal corporation with a statutory mandate to procure and award contracts for the construction of public buildings in the City of Chicago, and to oversee the construction of those public buildings until they are turned over to the user agency that will own and operate each new facility.

This is the first page of text of Book 1, which along with Book 2, Book 3, and the project drawings, comprise the PBC's construction contract. The balance of this Book 1 provides a brief description of the project, instructions for completing and submitting your bid, the bid pages, and the forms which must accompany your bid. Book 2 is the Standard Terms and Conditions of the contract. Book 3 is the Technical Specifications for the work to be performed on this project. The architect or engineer for the project will provide the drawings and other documents that may be necessary for you to bid on and/or perform the work. Each of the Books, along with the drawings and any other documents prepared by the architect or engineer, are Contract Documents. Collectively, the Contract Documents comprise the Contract. The Contract Documents are defined in Section 1 of Book 2, Standard Terms and Conditions.

#### II. PROJECT INFORMATION

#### A. General Information

1. Bids will be received by the Public Building Commission of Chicago for the following Project in accordance with the Contract Documents set forth below:

#### CONTRACT NO. C1607

# CHICAGO DEPARTMENT OF TRANSPORTATION CAPITAL PROGRAM ALLEYS (VARIOUS LOCATIONS): PACKAGE 1 CHICAGO, IL PBC PROJECTS #22356A-G CDOT PROJECT #S-3-356

#### 2. General Description of Scope of Work:

This Program includes reconstruction of alley sewers, subgrade and pavement utilizing "Green" construction materials and methods implemented by the City of Chicago, full depth alley pavement reconstruction of City of Chicago alleys. In addition, the Work includes proper handling and disposal of onsite material, portland cement concrete base course, hot-mix asphalt, surface course, sewer and drainage structures, sewer cleaning and televising, vortex restrictors, concrete curb and gutter, concrete sidewalks and ADA Ramps various depths, concrete driveways, concrete garage aprons, concrete alleys, premolded rubber speed humps, permeable concrete block pavers, bedding & void opening aggregates for permeable concrete block pavers, geotechnical fabric, topsoil, and hydraulic seeding.

- 3. Construction Budget for Base Work Only: \$2,500,000.00 to \$2,800,000.00 (including Allowances and Commission's Contract Contingency Funds).
- 4. User Agency: City of Chicago Department of Transportation (CDOT)
- 5. Project is located in Wards: 33, 40, 44, 47, and 50
- 6. For purposes of the community hiring requirement, "Project Community Residents" shall mean persons domiciled within the Project Community Areas as designated on "Exhibit# 3 Project Community Area Map."
- 7. Requests for Information: Bidders are to submit requests for information, in writing, via email to the attention of Mr. James Borkman. PBC Contract Officer at: iames.borkman@citvofchicago.org.
- 8. Contract Documents Availability: Documents are available at: Cross Rhodes Reprographics d/b/a Cross Rhodes Print & Technologies, 30 Eisenhower Lane North, Lombard, Illinois 60148. Contact name: Dan Rust. Telephone number: (630) 963-4700 ext 309.

Cross Rhodes Print & Technology Planroom: <a href="https://www.x-rhodesplanroom.com/">https://www.x-rhodesplanroom.com/</a>

- 9. Pre-Bid Meeting Date, Time, and Location: April 11, 2024, at 10:00a.m. via **ZOOM** virtual meeting platform. For meeting details, refer to Section II.A.20.
- 10. Technical Review Meeting Date, Time, and Location: April 11, 2024, at 10:30a.m. via **ZOOM** virtual meeting platform. For meeting details, refer to Section II.A.20.
- 11. Site Visit Meeting Date, Time, and Location:

Bidders shall be responsible for inspecting the Sites to become familiar with the conditions relating to the Work to be performed, the facilities involved, and the site logistics required for the successful performance of this Contract. Failure of the Bidders to visit the Sites shall not relieve or alter the Bidder's responsibility for completing the Work as required by the Contract Documents.

#### \*NOTES REGARDING MEETINGS:

- a. Meetings referenced in Items #9, 10, and 11 above are NOT mandatory.
- b. Subcontractors and Suppliers are encouraged to attend the meetings.
- c. Proper PPE must be worn at all times on the site.
- d. Bidders shall comply with all COVID-19 protocols in accordance with City of Chicago and CDC guidelines.
- 12. **Bid Due Date and Public Bid Opening Date, Time, and Location**: Bids Due: Bids are due **TUESDAY, MAY 7, 2024 at 11:00a.m.** and a Public Bid Opening will be held immediately following receipt of bids via ZOOM virtual meeting platform. For meeting details, refer to Section II.A.20.

13. Amount of Bid Deposit: 5% amount of bid

14. Document Deposit: N/A

15. Cost for Additional Documents (per set): At the Contractor's own expense.

16. MBE/WBE Contract Goals: 26% MBE and 6% WBE

17. Source of Funding: City of Chicago – Department of Transportation (CDOT)

18. **Pre-Award Meeting Date, Time, and Location:** A Pre-Award is tentatively scheduled for **Thursday, May 9, 2024 at 11:00 a.m.** via ZOOM virtual meeting platform. For meeting details, refer to Section II.A.20.

For the Pre-Award Meeting, the Lowest Responsive and Responsible Bidder shall be required to:

- a. Have, at minimum, the Project Executive, Project Manager (if known), and Cost Estimator in attendance at the meeting
- b. Invite principals of all MBE/WBE Subcontractors listed on Schedule D
- c. Provide and be prepared to discuss the Schedule of Values for the project
- d. Provide a list of Pre-Award meeting attendees in advance of the meeting
- 19. **Notice of Award** is anticipated to be issued following May 2024 PBC Board of Commissioners Meeting. The successful General Contractor will be required to return a compliant Certificate of Insurance and Payment and Performance Bond within seven (7) days of the issuance of the Notice of Award.
- 20. All meetings referenced throughout this document will be hosted on ZOOM virtual meeting platform. To join click on the link or call the number below:

Meeting Link: CDOT Capital Program – Alleys (Various) – PACKAGE 1

Meeting Phone Number:312-626-6799Meeting ID:811 2910 6143Meeting Passcode:None required

#### B. Mandatory Project Specific Contractor Staffing Requirements

The Contractor shall assign a Project Manager and/or a Superintendent to the Project effective as of the date of Notice to Proceed and effective until Final Acceptance. The Project Manager and/or Superintendent must be at the Project Site full time from the date of commencement of construction activities through Final Completion and Acceptance of the Work, including the completion of all Punch List Work, during Work Activities. Project Manager and Superintendent can be same individual.

Date of Issue: March 28, 2024 3 of 70

#### C. Scheduling Software Requirements

The Contractor shall utilize Primavera P6 Scheduling Software or other format approved by the Commission.

### D. Online Collaboration and Documentation Management System Requirements

The Contractor shall use PBC's designated On-line Collaboration and Document Management system to track the Work, manage the Project, and follow the Commission's procedures for electronic submission and receipt of documents as directed by the Commission Representative.

#### E. Time of Completion

Substantial Completion must be achieved no later than October 31, 2024. Schedule Milestones must be completed as follows:

Milestor	ne Descriptions	Milestone Dates
Schedul	e Milestone #1:	7/1/2024
•	Milestone #1 Pre-Construction, including Construction Submittals, Material and Equipment Procurement, Schedule Preparation, Mobilization, Utility Coordination, etc.	
(Commen	cement Date: May 14, 2024)	
Substan	tial Completion:	10/31/2024
•	Substantial Completion: Alley reconstruction and associated work.	
	scement Date: July 1, 2024) – (Work may commence upon completion and acceptance ne 1 per alley location)	

#### F. Commission's Contract Contingency

- 1. The Commission's Contract Contingency for this Project is: \$350,000.00
- 2. The Commission has established a Contract Contingency for the exclusive use of the Commission, at the Commission's sole discretion. The Commission's Contract Contingency sum shall be included as an allowance in the Base Bid. In the event that any or all of the Commission's Contract Contingency remains unused at the completion of the Work, the Commission will issue a deductive Change Order so that any such unused portion of the Commission's Contract Contingency shall remain with the PBC.

#### G. Copies of Drawings and Specifications

The Contractor is responsible for obtaining copies of Drawings and Specifications at its own cost.

#### H. Liquidated Damages

- 1. The Contractor agrees that the Work must be executed regularly and diligently to ensure completion within the time specified in Paragraph E above. The Contractor and the Commission understand and agree that the time for the completion of the Work described herein is reasonable time. If the Contractor neglects, fails or refuses to complete the Work within the time specified, or any proper extension granted by the Commission, then the Contractor and its surety do hereby agree to pay to the Commission the amount of \$500.00 per day for failure to achieve Substantial Completion by the specified date, and \$500.00 per day for failure to achieve each of the milestone dates. Failing to complete the work according to the time stipulated above will result in breach of contract and will result in Liquidated Damages being assessed each and every Day after the time stipulated in the Contract for completing the Work.
- 2. The Commission may recover liquidated damages by deducting the amount out of any monies due or that may become due the Contractor. Liquidated damages, if any, will be calculated on completion of the Work and submission of the Contractor's final pay request.
- 3. Substantial Completion of the Work is defined in Book 2, Section 1.01.37.

Date of Issue: March 28, 2024 4 of 70

#### I. Prevailing Wage Rates

 Not less than the prevailing rate of wages as determined by the Illinois Department of Labor shall be paid to all laborers, workers and mechanics performing work under this contract. Prevailing wage rates in effect at the time of issuance of these Contract Documents are attached to Book 1 as Exhibit 1. One resource for determining the current prevailing wage rate is the Internet site <a href="https://www.illinois.gov/idol">https://www.illinois.gov/idol</a> maintained by the State of Illinois Department of Labor.

#### III. INSTRUCTIONS FOR BIDDERS

#### A. Examination of Documents By Bidder

The Bidder shall, before submitting its bid, carefully examine all Contract Documents, including but not limited to, the Project Information, Instructions to Bidders, and Execution Documents (Book 1); Standard Terms and Conditions (Book 2); Technical Specifications (Book 3); plans; drawings; Addenda (if any); and bonds. The Bidder will be responsible for all errors in its bid resulting from failure or neglect to comply with these instructions.

The PBC requests that all questions related to this solicitation be submitted in writing via email to the attention of James Borkman at <a href="mailto:james.borkman@cityofchicago.org">james.borkman@cityofchicago.org</a> no later than **April 26, 2024.** 

#### B. Interpretations of Addenda

The Commission will not furnish oral interpretations of Contract Documents, before or subsequent to the award of a contract. If an interpretation is desired by a prospective Bidder, the interpretation should be requested in a letter addressed to the PBC, ATTN: James Borkman, Contract Officer or via email to: james.borkman@cityofchicago.org.

Every interpretation or revision will be in the form of an addendum to the Contract Documents and, when issued, will be on file in the office of the Commission and available on PBC's website at: <a href="http://www.pbcchicago.com">http://www.pbcchicago.com</a>. It shall be the Bidder's responsibility to inquire as to the addenda issued. All such addenda shall become part of the Contract and attached thereto. The Bidder's failure to acknowledge in writing any issued addenda on the Contractor's Bid page, Section IV. A. (Bid and Execution Documents-Contractor's Bid), shall result in the Commission finding the bid non-responsive and rejecting the bid. The Commission shall not allow any Bidder to acknowledge any such addenda, in writing or orally, after Bidder has submitted its bid to the Commission.

#### C. Pre-Qualification of Bidders

- 1. Unless otherwise indicated in Part II "Project Information", the Commission has previously issued Request for Qualifications (RFQ) to approve the qualifications of firms to perform work on the Project. Responses to the RFQ were evaluated by the Commission on the basis of the criteria set forth in the RFQ. Notice of pre-qualification has been provided by the Commission to all firms "pre-qualified", and only firms that have received notification of pre-qualification are eligible to bid on this Contract. Pre-qualified firms are eligible to bid either as the entity that was pre-qualified or as a joint venture with another firm, provided that the pre-qualified firm has a controlling interest in the joint venture.
- 2. The Commission reserves the right to take such steps as it deems necessary to determine the continuing qualifications of the Bidder to adequately perform the requirements of the Contract, and the Bidder shall furnish to the Commission all information and data requested for this purpose. Failure of the Bidder to cooperate with the Commission in its investigation or submit any additional documents requested by the Commission shall be grounds for disqualification.

#### D. Evidence of Continuing Qualifications of Bidder

- 1. The Commission reserves the right to refuse to award a Contract to any person, firm, or corporation that is in arrears or is in default to the Commission upon any debt or contract, or that is a defaulter, as surety or otherwise, upon any obligation to the Commission, or had failed to perform faithfully any previous contract with the Commission, or any of the User Agencies on whose behalf the PBC constructs public buildings.
- 2. The Bidder, if requested, must present within a reasonable time, as determined by the Commission, evidence satisfactory to the Commission of performance ability and possession of necessary facilities, pecuniary resources, and adequate insurance to comply with the terms of these specifications and Contract Documents.
- 3. The Bidder must provide the following item(s) with your Bid Submission:
  - a. Copy of current Contractor's General Contractor License.

Date of Issue: March 28, 2024 5 of 70

Failure to submit these items may deem the Bid unresponsive. Licenses may be that of the Prime, Joint Venture Partner (if any), and/or Sub-Contractor performing the work.

#### E. Preparation of Bid

- 1. A fully searchable .pdf of Project Information, Instructions, and Execution Documents (Book 1) shall be prepared with original signatures and notarizations wherever required.
- 2. All bids must be prepared on forms supplied by the Commission and shall be subject to all requirements of the Contract Documents. Unless otherwise stated, all blank spaces on the bid page or pages, applicable to the subject specification, should be correctly filled in. All bids must be regular in every respect and no interlineations, excisions or special conditions shall be made by the Bidder.
- The Bidder's name, address, telephone and fax number should be clearly written on the front cover of Book 1 submitted.
- 4. When required by the Contract Documents, the Bidder may attach supporting documentation or additional information to the back of the form to which it refers.
- 5. The Commission may consider as irregular, and at its option reject, any bid on which there is an alteration of or departure from the bid form hereto attached.
- 6. The Bid Documents shall include the following:
  - a. Contractor's Bid Form
  - b. Bid Guarantee (Bond)
  - c. Acceptance of the Bid
  - d. Basis of Award (Award Criteria)
  - e. Schedule of Prices
  - f. Affidavit of Non-collusion
  - g. Schedule B Joint Venture Affidavit with supporting documentation (if applicable)
  - h. Schedule C Letter of Intent from MBE/WBE
  - i. Schedule D Affidavit of General Contractor Regarding MBE/WBE Participation
  - j. Schedule E Request for Waiver from MBE/WBE Participation (if applicable)
  - k. Proof of ability to Provide Payment and Performance Bond
  - I. Proof of ability to Provide Insurance
  - m. General Contractors License
- 7. The Apparent Low Bidder is required to submit a fully executed Disclosure of Retained Parties within five (5) days after bid opening.

#### F. Bid Deposit

- 1. The Bid must be accompanied by a "Bid Deposit" in the amount set forth in Part II.A. "General Project Information" to ensure:
  - a. Non-withdrawal of the bid after date and time of opening.
  - b. The furnishing of the Performance and Payment Bond and evidence of the required insurance coverage by the successful Bidder as required by the Contract Documents.
- 2. The guarantee shall be made by bid bond, certified check or cashier's check payable to the order of the Public Building Commission of Chicago. No bid will be considered unless it is accompanied by the required guarantee. Cash deposits will not be accepted.

Date of Issue: March 28, 2024 6 of 70

3. The bid bonds, certified checks, or cashier's checks of unsuccessful Bidders will be returned as soon as practicable after the opening of the bids; however, the deposits of the three (3) lowest Bidders shall be retained until the Commission awards the Contract to one of them, or for any reason rejects all bids.

#### G. Bidder's Execution of Bid

- 1. The Bidder must execute the Bid in two (2) original counterparts.
- 2. Bids must be submitted with original signatures in the space provided on the appropriate Part IV.M. "Acceptance of the Bid." Bids not properly signed shall be rejected.
- 3. If Bidder is a corporation, the President and Secretary must execute the bid. In the event that this bid is executed by other than the President, attach hereto a certified copy of that section of the Corporate By-Laws or other authorization by the Corporation that permits the person to execute the offer for said corporation.
- 4. If Bidder is a partnership, all partners must execute the bid, unless one partner has been authorized to sign for the partnership, in which case, evidence of such authority satisfactory to the Commission must be submitted.
- 5. If Bidder is a sole proprietorship, the sole proprietor must execute the bid.
- 6. A "Partnership," "Joint Venture," or "Sole Proprietorship" operating under an Assumed Name must be registered with the Illinois county in which it is located, as provided in 805 ILCS 405 (1992).

#### H. Affidavit of Non-Collusion

Each Bidder shall fully execute an affidavit, in the form provided, to the effect that the Bidder has not colluded with any other person, firm, or corporation in regard to any bid submitted. Such affidavit shall be attached to the bid.

#### I. MBE and WBE Commitments

Contract specific goals for MBE and WBE participation is a minimum of 26% MBE and 6% WBE, respectively.

Each Bidder, which is a MBE/Non-MBE joint venture, shall submit with its Bid a completed **Schedule D**-Affidavit of General Contractor regarding M/WBE Participation and Schedule B- Affidavit of Joint Venture (if applicable) as found in Book 2 Section 23.05a (2, 3, 4) describing the extent to which Minority Business Enterprise (MBE) and Women Business Enterprise (WBE) firms will participate in the Contract.

The apparent low bidder must provide complete **Schedule C**- Letter of Intent from M/WBE to Perform as a Subcontractor, Subconsultant, or Material Supplier, including current certification letter for each MBE and WBE firm included in its bid, within 5 Days of the date set for bid opening.

Please refer to Exhibit 4 – Assist Agencies. Assist Agencies are comprised of chambers of commerce and not-for-profit agencies that represent the interest of small, minority- and/or women-owned businesses.

#### J. Local Business Subcontracting Participation and Community Hiring

In order to ensure that local businesses that provide subcontracting work to General Contractors on Commission projects and residents of the project communities are provided with the opportunity to benefit from Commission contracts, the Commission requires the following:

#### 2. Local Subcontracting Requirement

- a. General Contractors that are Local Businesses (as defined below) are required to award 25% of the Work under their contract with the Commission to subcontractors that are Local Businesses.
- b. General Contractors that are not Local Businesses are required to award 35% of the Work under their contract with the Commission to subcontractors that are Local Businesses.
- c. A Local Business is one that: 1) owns or leases a functioning business office and/or operations facilities within the City of Chicago (for City-funded projects) or the County of Cook (for Non-City-funded projects); 2) is registered and licensed to do business in the City of Chicago (for City-funded projects) or the County of Cook (for Non-City-funded projects); 3) employs City of Chicago residents (for City-funded projects) or Cook County residents (for Non-City-funded projects); and 4) is subject to City of Chicago taxes (for City-funded projects) or Cook County taxes (for Non-City-funded projects). In the event that the Commission performs a project for a unit of local government that operates in multiple municipalities, such as the Metropolitan Water Reclamation District, "Local Business" shall be defined in the bid documents for that project. The source of funding for the project is identified in Section II.A.18 above.

Date of Issue: March 28, 2024 7 of 70

- 3. Community Hiring Requirement. At least 7.5% of the project labor must be performed by "Project Community Residents" as defined in Section II.A.6 and included on the "Project Community Area Map" in Exhibit #3. The aggregate hours of Work to be performed by the Contractor and Subcontractors under this Contract may be complied through residents who are trade or non-trade workers. These positions may include but are not limited to trade workers, field engineer, superintendent, project manager, security, data entry clerks, schedulers, traffic monitoring personnel, and site administrative support staff. In order to comply with the Community Hiring requirement, the Contractor must hold a minimum of (2) application intake sessions in the designated Project Community as depicted on Exhibit (3) and compile an applicant database.
- 4. {INTENTIONALLY OMITTED}

#### K. Disclosure of Retained Parties

The apparent low Bidder shall submit a fully-executed Disclosure of Retained Parties pursuant to the instructions on the document within five (5) days of receipt of notice to provide such Disclosure.

#### L. Submission of Bid

- One (1) complete copy of all bid documents, including Bid Deposit in the amount listed in Section II. General Project Information, and with original signatures (signed in blue ink or Digital Signature), shall be submitted electronically, in a single searchable .pdf via email to: <a href="mailto:bids@pbcchicago.com">bids@pbcchicago.com</a> <a href="mailto:and-original-signature">and james.borkman@cityofchicago.org</a>.
- 2. Bidders who are unable to submit their bids electronically may request instructions for submitting a "hard copy" of their bid in writing to James Borkman, Director of Procurement at <a href="mailto:james.borkman@cityofchicago.org">james.borkman@cityofchicago.org</a>.
- 3. Bids received prior to the advertised hour of opening will be securely kept by the Commission.
- 4. Written modifications of bids will be considered only if received prior to the time stated for receipt of Bids. Such modifications must be submitted in a sealed envelope and marked in the same manner as a bid. IN ADDITION, the envelope must state "BID MODIFICATIONS TO SEALED BID" on the lower left-hand corner of the envelope in which the bid modification is enclosed, so that the modification will be recognized to prevent its being opened prior to scheduled public opening of bids. Telephonic or oral modifications will not be considered. Bidders are cautioned that modifications which are not explicit, and which are in any sense subject to misinterpretation shall make the bid so modified or amended subject to rejection.

#### M. Withdrawal of Bids before Bid Opening

Any Bidder may withdraw its bid by letter, e-mail request, or by personally securing, with proper identification, the submitted bid at any time prior to the time fixed for opening of bids. A telephonic request to withdraw a bid will not be considered.

#### N. Opening of Bids

At the time and place fixed for the opening of bids, the Commission will cause to be opened and publicly read aloud every bid received within the time set for receiving bids irrespective of any irregularities therein. Bidders and other persons or representatives properly interested may be present (virtually).

#### O. Evaluation of Bids

- 1. The Commission reserves the right to check all calculations and to correct all extensions in case of error in order to determine the correct amount of the Total Base Bid and/or the total amount of any other schedule required.
- 2. Along with reviewing the calculations of each bid, the Commission will evaluate each Bidder's responsiveness to all Bid requirements and responsibility.
- 3. The Commission may require that the Apparent Low Bidder and any other bidder submit a breakdown of their bids by CSI Division or other appropriate basis. The Commission may also require the Apparent Low Bidder, or any other bidder, to attend a pre-award meeting to review their bids in detail.

#### P. Basis of Award

1. Award will be made to the responsible Bidder submitting the Lowest Award Criteria Figure and otherwise responsive to all the requirements of the Contract Documents.

Date of Issue: March 28, 2024 8 of 70

#### Q. Performance and Payment Bond and Insurance

- Each Bidder shall furnish proof of its ability to provide the bonds and insurance required by the Contract with its bid. With respect to the payment and performance bonds, a letter from the Bidder's surety affirming the surety's willingness to provide the Bidder's bonds is sufficient. With respect to the insurance, either a letter from the Bidder's insurer, or a certificate showing that the Bidder currently possesses the required coverage, is sufficient.
- 2. The Contractor must provide and maintain at Contractor's own expense, the minimum insurance coverage and requirements specified in the attached Exhibit 2, insuring all operations related to the Contract. The insurance must remain in effect from the date of the Notice to Proceed until Substantial Completion of the project, during completion of Punch List, as well as any time the Contractor or its Subcontractors return to perform additional work regarding warranties or for any other purpose, unless otherwise noted in the requirements.
- 3. Upon approval by the Commission to award, and within seven (7) days after being given notice, the successful Bidder must execute and deliver to the Commission the Performance and Payment Bond in the form included in the Contract Documents, and evidence of the required insurance coverage.
- 4. The Performance and Payment Bond shall be in the form provided herein, in the full amount of the Contract Price and shall be security for the faithful performance of the Contract and payment of all persons, firms, or corporations to whom the Contractor may become legally indebted for labor, material, facilities or services of any nature, employed or used by it in performing the Work. The current power of attorney for the persons who sign for any surety company shall be attached to such bond. Such power of attorney shall be sealed and certified with a "first hand signature" by an officer of the surety. A facsimile signature will not be accepted by the Commission. The Commission reserves the right to approve the surety company.
- 5. The failure of the successful Bidder to supply the required Performance and Payment Bond or evidence of the required insurance coverage within seven (7) days of notice, or within such extended period as the Commission may grant based upon reasons determined sufficient by the Commission, shall constitute a default and the Commission may either award the Contract to the next lowest responsible bidder or re-advertise for bids. The difference between the amount of its bid and the amount for which a contract for the work is subsequently executed may be charged against the Bidder, irrespective of whether the amount thus due exceeds the amount of the bid security. If a more favorable bid is received by re-advertising, the defaulting Bidder shall have no claim against the Commission for a refund. Because of the difficulty of ascertaining the damage caused to the Commission, such sum shall be considered liquidated damages and shall not constitute a penalty. The election by the Commission to grant an extension to the period allowed for the bidder to provide an acceptable performance and payment bond and/or evidence of insurance coverage shall not entitle the bidder to an extension of time required to complete the Work.

#### R. Protests

1. The bidder shall submit any protests or claims regarding this solicitation to the office of the Commission's Executive Director located at 50 W. Washington, Room 200, Chicago, Illinois 60602. A pre-bid protest must be filed no later than five calendar (5) days before the bid opening date, a pre-award protest must be filed no later than ten (10) days after the bid opening date, and a post-award protest must be filed no later than ten (10) days after the award of the Contract.

BID PROTEST ACTIONS	TERM
Type of Protests Allowed: Pre-Bid, Pre-Award, Post-Award	All
Pre-Bid Protest Timing	No later than five (5) calendar days before Bid Opening
Pre-Award (Bid Results) Protest Timing	No later than ten (10) calendar days after Bid Opening
Post-Award Protest Timing	No later than ten (10) calendar days after Award
Adjudicator Role	Executive Director

2. All protests or claims must set forth the name and address of the protester, the contract number, the grounds for the protest or claim, and the course of action that the protesting party desires that the Executive Director take.

#### S. Licensing

In addition to all other applicable licenses and certifications, the general contractor is required to submit a copy of its General Contractor License issued by the Department of Buildings of the City of Chicago.

Date of Issue: March 28, 2024 9 of 70

#### T. Award of Contract, Cancellation, or Rejection of Bids

- 1. Award will be made to the responsible Bidder submitting the Lowest Award Criteria Figure as noted in Section III.P. Basis of Award above and otherwise responsive to all the requirements of the Contract Documents.
- 2. The Bidder agrees its bid shall remain valid for a period of up to 60 days after receipt of bid and the bid cannot be withdrawn until that time.
- The Bidder to whom the award is made will be notified as soon as practicable after the Commission approves award of the Contract. This written notification constitutes the Notice of Award and acceptance of the bid submitted.
- 4. If written notice of the acceptance of this Bid is mailed, faxed, e-mailed or otherwise delivered to the undersigned within the time noted herein, or at any time thereafter before this Bid is withdrawn, the undersigned agrees to enter into a Contract with the Public Building Commission of Chicago with the Bid as accepted. The undersigned agrees to give a Performance and Payment Bond as specified in the Contract Documents, with good and sufficient surety or sureties, and to furnish the required insurance, all within five (5) days after given Notice of Award.
- 5. Upon award of Contract, the Commission will process the Contract for final execution.
- The Commission reserves the right to reject any and all bids wherever such rejection is in the best interest of the Commission.
- 7. The Commission reserves the right to waive any informality in bids received whenever it determines such waiver is in the best interest of the Commission.
- 8. The Commission reserves the right to cancel the solicitation whenever it determines such cancellation is in the best interest of the Commission.

#### U. Alternates

{INTENTIONALLY OMMITTED}

Remainder of Page Left Blank Intentionally

Date of Issue: March 28, 2024 10 of 70

#### IV. BID AND EXECUTION DOCUMENTS

#### A. CONTRACTOR'S BID

The Contractor hereby acknowledges receipt of the Contract Documents for Contract No. C1607, including, but not limited to, a) Project Information, Instructions to Bidders, and Execution Documents (Book 1), b) Standard Terms and Conditions (Book 2), c), Technical Specifications (Book 3), d) Plans and Drawings, and e) Addenda Nos. (None unless indicated here)

Further, the Contractor, having inspected the Sites and become familiar with the conditions affecting the cost of the Work and with the requirements of the Contract, hereby proposes to furnish all labor, necessary tools, materials and other work necessary to perform and complete in a workmanlike manner the CDOT CAPITAL PROGRAM – ALLEYS (Various Locations): PACKAGE 1 located at the Sites designated as required by and in strict accordance with the Contract Documents for Total Base Bid indicated on the next page. The Total Base Bid as accepted by the Commission and awarded to the Contractor shall be the Contract Price listed on the next page.

The agreement between the parties includes not only this instrument, but also the remaining Contract Documents as described in the Standard Terms and Conditions, and all of which shall be binding on the parties hereto.

Time is of the essence of this Contract. The Contractor agrees that it will commence the performance of the Work on the date set forth in the Notice to Proceed issued by the Commission and that it will complete the Work within the time set forth in Part II "Project Information".

The Contract Price, as adjusted from time to time pursuant to the Contract Documents, shall be full compensation to the Contractor for having well and faithfully completed the Work, free and clear of all claims, liens, and charges whatsoever, of any kind or nature, and in full compliance with the Contract.

Payment for the Work will be made in the manner set forth in Book 2 Standard Terms and Conditions.


The Contractor warrants that it has not employed any person to solicit or secure this Contract upon any agreement for a commission, percentage, brokerage, or contingent fee. Breach of this warranty shall give the Commission the right to terminate the Contract, or, at its discretion, to deduct from the Contract Price or consideration the amount of such commission, percentage, brokerage, or contingent fees. This warranty shall not apply to any commission payable by the Contractor upon contracts or sales secured or made through bona fide established commercial or selling agencies maintained by the Contractor for the purpose of securing business.

The Contractor, being duly sworn, deposes and says on oath that no disclosures of ownership interests have been withheld; the information provided therein to the best of its knowledge is current; and the undersigned proposes to furnish the insurance and the Performance and Payment Bond required by the Contract Documents.

Date of Issue: March 28, 2024 11 of 70

#### B. BID FORM - CDOT CAPITAL PROGRAM - ALLEYS (Various Locations) - Package 1 - BASE BID

Bidders <u>MUST</u> use the Excel File (available at the X-Rhodes Planroom: <a href="https://www.x-rhodesplanroom.com/">https://www.x-rhodesplanroom.com/</a>) to ensure accurate calculations for the Total Base Bid and Total Award Criteria.

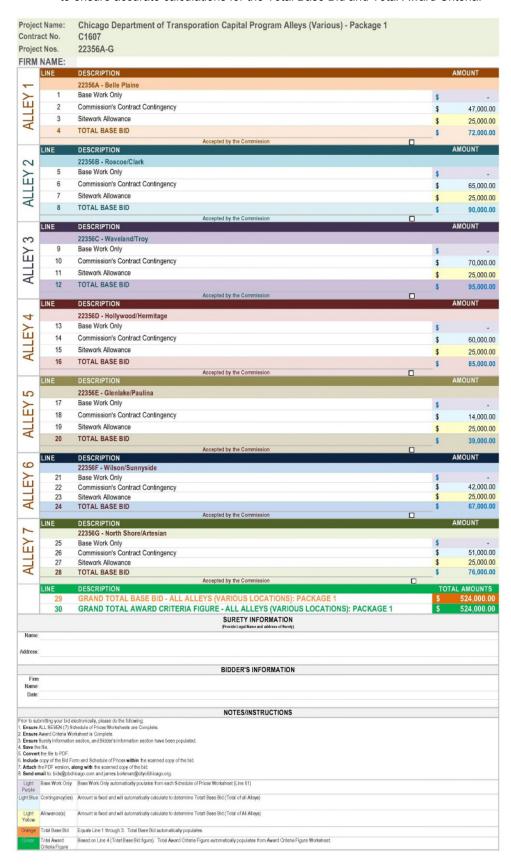

Date of Issue: March 28, 2024 12 of 70

#### C. SITE WORK ALLOWANCE SCHEDULE

#### CDOT CPAITAL PROGRAM - ALLEYS (Various) PACKAGE 1 - \$175,000.00

Item No.	Description of Work	Unit(s)	Unit Price
1	UST Removal (Tank < 2000 gal capacity), including UST Removal Permit.	Each	\$5,000.00
2	UST Removal (Tank 3,000-5,500 gal capacity), including UST Removal Permit.	Each	\$5,500.00
3	UST Removal (Tank 6,000-10,000 gal capacity), including UST Removal Permit.	Each	\$8,500.00
4	UST Removal (Tank > 10,000-15,000 gal capacity), including UST Removal Permit.	Each	\$9,500.00
5	UST Removal (Tank > 15,000 gal capacity), including UST Removal Permit.	Each	\$12,500.00
6	UST tank sludge removal and disposal (55-gallon drum), including UST Removal Permit.	Drums	\$450.00
7	Bulk UST pump out (Liquids), including transportation	Gallons	\$0.60
8	Waste characterization sample analysis for disposal authorization of soils removed under Allowance Schedule (Including Waste Profile Application)	Sample	\$1,500.00
9	Water analysis for full MWRDGC contaminants List	Each	\$750.00
10	Obtain MWRDGC discharge permit for Bulk disposal of contaminated liquid	Each	\$2,000.00
11	Contaminated water-hauling and disposal of drums	Drums	\$200.00
12	Pumping, transportation and disposal of contaminated water - bulk disposal	Gallons	\$0.60
13	Pumping, storage and disposal of contaminated water - bulk disposal by MWRDGC Permit	Gallons	\$0.10
14	Furnish and place geotextile filter fabric	Square Yard	\$8.00

#### NOTES:

- 1. All Work associated with the above allowance schedule shall be approved in writing by the Commission Representative prior to proceeding.
- 2. Authorized additional excavation and replacement material will be paid for in accordance with the above allowance schedule.
- 3. Authorized additional excavation means excavation below subgrade elevations shown in the Contract Documents, as determined by the Commission Representative.
- 4. The unit prices in this allowance schedule include all overhead, profit, and schedule impact costs.
- 5. All unused portions of the allowance funds must be returned to the Commission.

#### D. SCHEDULE OF PRICES

#### **SCHEDULE OF PRICES**

CDOT Capital Program - Alleys (Various Locations): Package 1 LOCATION: W. BELLE PLAINE AVE/W. IRVING PARK RD/N. PAULINA ST/N. ASHLAND AVE Ward 47

#### PBC PROJECT NO: 22356A

CDOT PROJECT NO.: B-3-356 - PBC CONTRACT C1607

Bidder's pricing for each line item should carry its share of the costs of work, plus its share of overhead and profit.

Bidders should avoid nominal pricing for some lines and enhanced pricing for other lines.

Bids that the PBC considers to be materially unbalanced will be rejected.

Line	Code Number	Description	Unit	Estimated Quantity	Unit Price	Cost
1	*****	EARTH EXCAVATION (SOIL TO CCDD FACILITY)	Cubic Yard	431		
2	*****	EARTH EXCAVATION (SOIL TO LANDFILL)	Cubic Yard	10		
3	44000100	PAVEMENT REMOVAL	Square Yard	19		
4	*****	DRIVEWAY AND ALLEY RETURN PAVEMENT REMOVAL	Square Yard	45		
5	44000300	CURB REMOVAL	Foot	61		
6	44000500	COMBINATION CURB AND GUTTER REMOVAL	Foot	85		
7	44000600	SIDEWALK REMOVAL	Square Foot	405		
8	CDOT4400020	ALLEY PAVEMENT REMOVAL	Square Yard	1291		
9	*****	GARAGE APRON REMOVAL	Square Foot	999		
10	20700220	POROUS GRANULAR EMBANKMENT (CA-1)	Cubic Yard	0		
11	31101100	SUB-BASE GRANULAR MATERIAL, TYPE B	Cubic Yard	223		
12	20800150	TRENCH BACKFILL	Cubic Yard	72		
13	CDOT3110030	PERVIOUS AGGREGATE SUBBASE	Cubic Yard	0		
14	*****	BEDDING & VOID OPENING AGGREGATES FOR PERMEABLE CONCRETE BLOCK PAVERS	Cubic Yard	0		
15	*****	CRUSHED STONE (TEMPORARY USE)	Ton	40		
16	35300200	PORTLAND CEMENT CONCRETE BASE COURSE, 7 IN	Square Yard	9		
17	35300400	PORTLAND CEMENT CONCRETE BASE COURSE, 9 IN	Square Yard	11		

Date of Issue: March 28, 2024 14 of 70

#### CDOT Capital Program - Alleys (Various Locations): Package 1 LOCATION: W. BELLE PLAINE AVE/W. IRVING PARK RD/N. PAULINA ST/N. ASHLAND AVE Ward 47

#### **PBC PROJECT NO: 22356A**

CDOT PROJECT NO.: B-3-356 - PBC CONTRACT C1607

Bidder's pricing for each line item should carry its share of the costs of work, plus its share of overhead and profit.

Bidders should avoid nominal pricing for some lines and enhanced pricing for other lines.

Bids that the PBC considers to be materially unbalanced will be rejected.

		that the PBC considers to be materially t	1		l.	
18	CDOT4230030	HIGH EARLY STRENGTH PORTLAND CEMENT CONCRETE ALLEY PAVEMENT, 8 INCH	Square Yard	1316		
19	CDOT4230010	HIGH EARLY STRENGTH PORTLAND CEMENT CONCRETE DRIVEWAY PAVEMENT, 8 INCH	Square Yard	0		
20	*****	HIGH EARLY STRENGTH PORTLAND CEMENT CONCRETE GARAGE APRON, 8 INCH	Square Foot	999		
21	*****	HIGH EARLY STRENGTH PORTLAND CEMENT CONCRETE SIDEWALK, 8 INCH	Square Foot	187		
22	******	PORTLAND CEMENT CONCRETE SIDEWALK, 8 IN	Square Foot	106		
23	*****	PORTLAND CEMENT CONCRETE SIDEWALK, 5 IN	Square Foot	282		
24	******	PORTLAND CEMENT CONCRETE ADA CURB RAMP, 5 IN	Square Foot	123		
25	*****	HIGH EARLY STRENGTH PORTLAND CEMENT CONCRETE ADA CURB RAMP, 8 INCH	Square Foot	0		
26	******	DRILL AND GROUT DOWELS AND TIE BARS	Each	180		
27	*****	PORTLAND CEMENT CONCRETE COLLAR FOR PERMEABLE BLOCK PAVERS, POROUS TILE PAVERS, OR PERVIOUS HMA	Foot	0		
28	******	PERMEABLE CONCRETE BLOCK PAVERS	Square Foot	0		
29	******	GREEN ALLEY IDENTIFIER CONCRETE STAMP	Each	2		
30	40600200	BITUMINOUS MATERIALS (TACK COAT)	Pound	9		
31	4060105	HOT-MIX ASPHALT SURFACE COURSE, IL-9.5L, MIX "C", N30 (CDOT)	Ton	0		
32	40603085	HOT-MIX ASPHALT BINDER COURSE, N70	Ton	0		
33	******	HOT-MIX ASPHALT, REMOVE AND RESURFACE, N30	Square Yard	0		
34	*****	HOT-MIX ASPHALT SURFACE COURSE, PATCH, N30 (HAND METHOD)	Ton	2		

Date of Issue: March 28, 2024
PBC: C1607\_CDOT Capital Program - Alleys (Various Locations) Package 1\_Book 1 Instructions to Bidders

### CDOT Capital Program - Alleys (Various Locations): Package 1 LOCATION: W. BELLE PLAINE AVE/W. IRVING PARK RD/N. PAULINA ST/N. ASHLAND AVE Ward 47

#### **PBC PROJECT NO: 22356A**

CDOT PROJECT NO.: B-3-356 - PBC CONTRACT C1607

Bidder's pricing for each line item should carry its share of the costs of work, plus its share of overhead and profit.

Bidders should avoid nominal pricing for some lines and enhanced pricing for other lines.

Bids that the PBC considers to be materially unbalanced will be rejected.

	•	that the FBC considers to be materially t			1.	1
35	******	HOT-MIX ASPHALT SURFACE COURSE, PATCH, N70 (HAND METHOD)	Ton	2		
36	60600605	CONCRETE CURB, TYPE B	Foot	61		
37	******	HIGH EARLY STRENGTH PORTLAND CEMENT CONCRETE COMBINATION CURB AND GUTTER, TYPE B-V.12	Foot	54		
38	CDOT 6060020	COMBINATION CONCRETE CURB AND GUTTER, TYPE B-V.12	Foot	31		
39	*****	MANHOLE, 3 FT DIAMETER, TYPE A, FRAME AND CLOSED LID (CITY OF CHICAGO)	Each	0		
40	*****	CATCH BASINS, TYPE A, SPECIAL, 3 FT DIAMETER, TYPE 1 FRAME, OPEN LID (CITY OF CHICAGO)	Each	0		
41	CDOT6020010	CATCH BASINS, TYPE A, 4 FT DIAMETER, TYPE 1 FRAME, OPEN LID (CITY OF CHICAGO)	Each	2		
42	******	DRAINAGE AND UTILITY STRUCTURES TO BE ADJUSTED	Each	2		
43	******	VORTEX RESTRICTOR	Each	1		
44	*****	STORM SEWERS, EXTRA STRENGTH VITRIFIED CLAY PIPE, 8 IN	Foot	0		
45	******	STORM SEWERS, DUCTILE IRON PIPE, 18 IN	Foot	106		
46	*****	STORM SEWERS, EXTRA STRENGTH VITRIFIED CLAY PIPE, 15 IN	Foot	0		
47	*****	STORM SEWERS, EXTRA STRENGTH VITRIFIED CLAY PIPE, 18 IN	Foot	0		
48	CDOT6050010	REMOVING MANHOLES	Each	1		
49	CDOT6050020	REMOVING CATCH BASINS	Each	1		
50	*****	SEWER CLEANING AND TELEVISING	Foot	211		
51	*****	CATCH BASINS, MANHOLES, WATER VALVES, ROUNDWAYS, AND INLETS TO BE CLEANED	Each	0		
52	60100085	GEOTECHNICAL FABRIC	Square Yard	0		

Date of Issue: March 28, 2024
PBC: C1607\_CDOT Capital Program - Alleys (Various Locations) Package 1\_Book 1 Instructions to Bidders

### CDOT Capital Program - Alleys (Various Locations): Package 1 LOCATION: W. BELLE PLAINE AVE/W. IRVING PARK RD/N. PAULINA ST/N. ASHLAND AVE Ward 47

#### **PBC PROJECT NO: 22356A**

CDOT PROJECT NO.: B-3-356 - PBC CONTRACT C1607

Bidder's pricing for each line item should carry its share of the costs of work, plus its share of overhead and profit.

Bidders should avoid nominal pricing for some lines and enhanced pricing for other lines.

Bids that the PBC considers to be materially unbalanced will be rejected.

			T-4-1 222	56A Belle Plain	_	
57	******	REMOVE AND RELOCATE SIGN PANEL AND POLE ASSEMBLY	Each	3		
56	******	PREMOLDED RUBBER SPEED HUMPS	Each	0		
55	*****	CONSTRUCTION SIGN	Square Foot	64		
54	*****	HYDRAULIC SEEDING	Square Yard	7		
53	CDOT2110010	PULVERIZED TOPSOIL MIX	Cubic Yard	4		

Date of Issue: March 28, 2024 17 of 70

#### **SCHEDULE OF PRICES - 22356B**

CDOT Capital Program - Alleys (Various Locations): Package 1
LOCATION: W. ROSCOE ST/W. BUCKINGHAM PL/N. CLART ST/N. HALSTED ST - Ward 44
PBC PROJECT NO.: 22356B

CDOT PROJECT NO.: B-3-356 – PBC CONTRACT C1607

Bidder's pricing for each line item should carry its share of the costs of work, plus its share of overhead and profit. Bidders should avoid nominal pricing for some lines and enhanced pricing for other lines.

Bids that the PBC considers to be materially unbalanced will be rejected.

Line	Code Number	Description	Unit	Estimated Quantity	Unit Price	Cost
1	*****	EARTH EXCAVATION (SOIL TO CCDD FACILITY)	Cubic Yard	306		
2	******	EARTH EXCAVATION (SOIL TO LANDFILL)	Cubic Yard	465		
3	44000100	PAVEMENT REMOVAL	Square Yard	0		
4	*****	DRIVEWAY AND ALLEY RETURN PAVEMENT REMOVAL	Square Yard	9		
5	44000300	CURB REMOVAL	Foot	0		
6	44000500	COMBINATION CURB AND GUTTER REMOVAL	Foot	0		
7	44000600	SIDEWALK REMOVAL	Square Foot	0		
8	CDOT4400020	ALLEY PAVEMENT REMOVAL	Square Yard	2270		
9	******	GARAGE APRON REMOVAL	Square Foot	996		
10	20700220	POROUS GRANULAR EMBANKMENT (CA-1)	Cubic Yard	0		
11	31101100	SUB-BASE GRANULAR MATERIAL, TYPE B	Cubic Yard	505		
12	20800150	TRENCH BACKFILL	Cubic Yard	0		
13	CDOT3110030	PERVIOUS AGGREGATE SUBBASE	Cubic Yard	0		
14	*****	BEDDING & VOID OPENING AGGREGATES FOR PERMEABLE CONCRETE BLOCK PAVERS	Cubic Yard	0		
15	******	CRUSHED STONE (TEMPORARY USE)	Ton	0		
16	35300200	PORTLAND CEMENT CONCRETE BASE COURSE, 7 IN	Square Yard	0		
17	35300400	PORTLAND CEMENT CONCRETE BASE COURSE, 9 IN	Square Yard	0		

Date of Issue: March 28, 2024

# CDOT Capital Program - Alleys (Various Locations): Package 1 LOCATION: W. ROSCOE ST/W. BUCKINGHAM PL/N. CLART ST/N. HALSTED ST - Ward 44 PBC PROJECT NO.: 22356B

#### CDOT PROJECT NO.: B-3-356 - PBC CONTRACT C1607

Bidder's pricing for each line item should carry its share of the costs of work, plus its share of overhead and profit. Bidders should avoid nominal pricing for some lines and enhanced pricing for other lines.

Bids that the PBC considers to be materially unbalanced will be rejected.

18	CDOT4230030	HIGH EARLY STRENGTH	Square	2270	
		PORTLAND CEMENT CONCRETE ALLEY PAVEMENT, 8 INCH	Yard		
19	CDOT4230010	HIGH EARLY STRENGTH PORTLAND CEMENT CONCRETE DRIVEWAY PAVEMENT, 8 INCH	Square Yard	0	
20	******	HIGH EARLY STRENGTH PORTLAND CEMENT CONCRETE GARAGE APRON, 8 INCH	Square Foot	996	
21	*****	HIGH EARLY STRENGTH PORTLAND CEMENT CONCRETE SIDEWALK, 8 INCH	Square Foot	0	
22	******	PORTLAND CEMENT CONCRETE SIDEWALK, 8 IN	Square Foot	74	
23	*****	PORTLAND CEMENT CONCRETE SIDEWALK, 5 IN	Square Foot	0	
24	*****	PORTLAND CEMENT CONCRETE ADA CURB RAMP, 5 IN	Square Foot	0	
25	*****	HIGH EARLY STRENGTH PORTLAND CEMENT CONCRETE ADA CURB RAMP, 8 INCH	Square Foot	0	
26	*****	DRILL AND GROUT DOWELS AND TIE BARS	Each	240	
27	******	PORTLAND CEMENT CONCRETE COLLAR FOR PERMEABLE BLOCK PAVERS, POROUS TILE PAVERS, OR PERVIOUS HMA	Foot	0	
28	*****	PERMEABLE CONCRETE BLOCK PAVERS	Square Foot	0	
29	*****	GREEN ALLEY IDENTIFIER CONCRETE STAMP	Each	4	
30	40600200	BITUMINOUS MATERIALS (TACK COAT)	Pound	0	
31	4060105	HOT-MIX ASPHALT SURFACE COURSE, IL-9.5L, MIX "C", N30 (CDOT)	Ton	0	
32	40603085	HOT-MIX ASPHALT BINDER COURSE, N70	Ton	0	
33	*****	HOT-MIX ASPHALT, REMOVE AND RESURFACE, N30	Square Yard	0	
34	*****	HOT-MIX ASPHALT SURFACE COURSE, PATCH, N30 (HAND METHOD)	Ton	0	

Date of Issue: March 28, 2024 19 of 70

# CDOT Capital Program - Alleys (Various Locations): Package 1 LOCATION: W. ROSCOE ST/W. BUCKINGHAM PL/N. CLART ST/N. HALSTED ST - Ward 44 PBC PROJECT NO.: 22356B

### CDOT PROJECT NO.: B-3-356 - PBC CONTRACT C1607

Bidder's pricing for each line item should carry its share of the costs of work, plus its share of overhead and profit. Bidders should avoid nominal pricing for some lines and enhanced pricing for other lines.

Bids that the PBC considers to be materially unbalanced will be rejected.

35	*****	HOT-MIX ASPHALT SURFACE COURSE, PATCH, N70 (HAND METHOD)	Ton	0	
36	60600605	CONCRETE CURB, TYPE B	Foot	0	
37	*****	HIGH EARLY STRENGTH PORTLAND CEMENT CONCRETE COMBINATION CURB AND GUTTER, TYPE B-V.12	Foot	0	
38	CDOT 6060020	COMBINATION CONCRETE CURB AND GUTTER, TYPE B-V.12	Foot	0	
39	******	MANHOLE, 3 FT DIAMETER, TYPE A, FRAME AND CLOSED LID (CITY OF CHICAGO)	Each	0	
40	*****	CATCH BASINS, TYPE A, SPECIAL, 3 FT DIAMETER, TYPE 1 FRAME, OPEN LID (CITY OF CHICAGO)	Each	0	
41	CDOT6020010	CATCH BASINS, TYPE A, 4 FT DIAMETER, TYPE 1 FRAME, OPEN LID (CITY OF CHICAGO)	Each	0	
42	*****	DRAINAGE AND UTILITY STRUCTURES TO BE ADJUSTED	Each	0	
43	*****	VORTEX RESTRICTOR	Each	0	
44	*****	STORM SEWERS, EXTRA STRENGTH VITRIFIED CLAY PIPE, 8 IN	Foot	0	
45	*****	STORM SEWERS, DUCTILE IRON PIPE, 18 IN	Foot	0	
46	*****	STORM SEWERS, EXTRA STRENGTH VITRIFIED CLAY PIPE, 15 IN	Foot	0	
47	*****	STORM SEWERS, EXTRA STRENGTH VITRIFIED CLAY PIPE, 18 IN	Foot	0	
48	CDOT6050010	REMOVING MANHOLES	Each	0	
49	CDOT6050020	REMOVING CATCH BASINS	Each	0	
50	*****	SEWER CLEANING AND TELEVISING	Foot	0	
51	*****	CATCH BASINS, MANHOLES, WATER VALVES, ROUNDWAYS, AND INLETS TO BE CLEANED	Each	0	
52	60100085	GEOTECHNICAL FABRIC	Square Yard	0	

Date of Issue: March 28, 2024 20 of 70

# CDOT Capital Program - Alleys (Various Locations): Package 1 LOCATION: W. ROSCOE ST/W. BUCKINGHAM PL/N. CLART ST/N. HALSTED ST - Ward 44 PBC PROJECT NO.: 22356B

#### CDOT PROJECT NO.: B-3-356 - PBC CONTRACT C1607

Bidder's pricing for each line item should carry its share of the costs of work, plus its share of overhead and profit. Bidders should avoid nominal pricing for some lines and enhanced pricing for other lines.

Bids that the PBC considers to be materially unbalanced will be rejected.

CDOT2110010	PULVERIZED TOPSOIL MIX	Cubic	0		
		Yard			
******	HYDRAULIC SEEDING	Square	0		
		Yard			
******	CONSTRUCTION SIGN	Square	64		
		Foot			
*****	PREMOLDED RUBBER SPEED	Each	1		
	HUMPS				
*****	REMOVE AND RELOCATE SIGN	Each	0		
	PANEL AND POLE ASSEMBLY				
		Total 2235	6B Roscoe/Cl	lark	
	******	******* HYDRAULIC SEEDING  ******** CONSTRUCTION SIGN  ******* PREMOLDED RUBBER SPEED HUMPS  ******** REMOVE AND RELOCATE SIGN	**************************************	**************************************	********         HYDRAULIC SEEDING         Square yard         0           ********         CONSTRUCTION SIGN         Square Foot         64 Foot           ********         PREMOLDED RUBBER SPEED Fach HUMPS         Each 1         1           *********         REMOVE AND RELOCATE SIGN Fach 0         0

Date of Issue: March 28, 2024 21 of 70

#### SCHEDULE OF PRICES - 22356C

CDOT Capital Program - Alleys (Various Locations): Package 1 LOCATION: W. WAVELAND AVE/ W. ADDISON ST/N. ALBANY AVE/N. TROY ST - Ward 33 PBC PROJECT NO.: 22356C

CDOT PROJECT NO.: B-3-356 - PBC CONTRACT C1607

Bidder's pricing for each line item should carry its share of the costs of work, plus its share of overhead and profit. Bidders should avoid nominal pricing for some lines and enhanced pricing for other lines. Bids that the PBC considers to be materially unbalanced will be rejected.

Line	Code Number	Description	Unit	Estimated Quantity	Unit Price	Cost
1	*****	EARTH EXCAVATION (SOIL TO CCDD FACILITY)	Cubic Yard	761		
2	*****	EARTH EXCAVATION (SOIL TO LANDFILL)	Cubic Yard	51		
3	44000100	PAVEMENT REMOVAL	Square Yard	16		
4	******	DRIVEWAY AND ALLEY RETURN PAVEMENT REMOVAL	Square Yard	47		
5	44000300	CURB REMOVAL	Foot	43		
6	44000500	COMBINATION CURB AND GUTTER REMOVAL	Foot	36		
7	44000600	SIDEWALK REMOVAL	Square Foot	120		
8	CDOT4400020	ALLEY PAVEMENT REMOVAL	Square Yard	1318		
9	*****	GARAGE APRON REMOVAL	Square Foot	2363		
10	20700220	POROUS GRANULAR EMBANKMENT (CA-1)	Cubic Yard	0		
11	31101100	SUB-BASE GRANULAR MATERIAL, TYPE B	Cubic Yard	229		
12	20800150	TRENCH BACKFILL	Cubic Yard	506		
13	CDOT3110030	PERVIOUS AGGREGATE SUBBASE	Cubic Yard	0		
14	*****	BEDDING & VOID OPENING AGGREGATES FOR PERMEABLE CONCRETE BLOCK PAVERS	Cubic Yard	0		
15	*****	CRUSHED STONE (TEMPORARY USE)	Ton	30		
16	35300200	PORTLAND CEMENT CONCRETE BASE COURSE, 7 IN	Square Yard	16		
17	35300400	PORTLAND CEMENT CONCRETE BASE COURSE, 9 IN	Square Yard	0		

### CDOT Capital Program - Alleys (Various Locations): Package 1 LOCATION: W. WAVELAND AVE/ W. ADDISON ST/N. ALBANY AVE/N. TROY ST - Ward 33

#### PBC PROJECT NO.: 22356C

#### CDOT PROJECT NO.: B-3-356 - PBC CONTRACT C1607

Bidder's pricing for each line item should carry its share of the costs of work, plus its share of overhead and profit.

Bidders should avoid nominal pricing for some lines and enhanced pricing for other lines.

Bids that the PBC considers to be materially unbalanced will be rejected.

	1	,	1	,	
18	CDOT4230030	HIGH EARLY STRENGTH PORTLAND CEMENT CONCRETE ALLEY PAVEMENT, 8 INCH	Square Yard	1336	
19	CDOT4230010	HIGH EARLY STRENGTH PORTLAND CEMENT CONCRETE DRIVEWAY PAVEMENT, 8 INCH	Square Yard	12	
20	*****	HIGH EARLY STRENGTH PORTLAND CEMENT CONCRETE GARAGE APRON, 8 INCH	Square Foot	2363	
21	*****	HIGH EARLY STRENGTH PORTLAND CEMENT CONCRETE SIDEWALK, 8 INCH	Square Foot	122	
22	******	PORTLAND CEMENT CONCRETE SIDEWALK, 8 IN	Square Foot	0	
23	******	PORTLAND CEMENT CONCRETE SIDEWALK, 5 IN	Square Foot	228	
24	******	PORTLAND CEMENT CONCRETE ADA CURB RAMP, 5 IN	Square Foot	30	
25	*****	HIGH EARLY STRENGTH PORTLAND CEMENT CONCRETE ADA CURB RAMP, 8 INCH	Square Foot	30	
26	*****	DRILL AND GROUT DOWELS AND TIE BARS	Each	155	
27	******	PORTLAND CEMENT CONCRETE COLLAR FOR PERMEABLE BLOCK PAVERS, POROUS TILE PAVERS, OR PERVIOUS HMA	Foot	0	
28	*****	PERMEABLE CONCRETE BLOCK PAVERS	Square Foot	0	
29	******	GREEN ALLEY IDENTIFIER CONCRETE STAMP	Each	3	
30	40600200	BITUMINOUS MATERIALS (TACK COAT)	Pound	54	
31	4060105	HOT-MIX ASPHALT SURFACE COURSE, IL-9.5L, MIX "C", N30 (CDOT)	Ton	1	
32	40603085	HOT-MIX ASPHALT BINDER COURSE, N70	Ton	2	
33	******	HOT-MIX ASPHALT, REMOVE AND RESURFACE, N30	Square Yard	100	
34	*****	HOT-MIX ASPHALT SURFACE COURSE, PATCH, N30 (HAND METHOD)	Ton	2	

Date of Issue: March 28, 2024
PBC: C1607\_CDOT Capital Program - Alleys (Various Locations) Package 1\_Book 1 Instructions to Bidders

#### LOCATION: W. WAVELAND AVE/ W. ADDISON ST/N. ALBANY AVE/N. TROY ST - Ward 33

#### PBC PROJECT NO.: 22356C

#### CDOT PROJECT NO.: B-3-356 - PBC CONTRACT C1607

Bidder's pricing for each line item should carry its share of the costs of work, plus its share of overhead and profit.

Bidders should avoid nominal pricing for some lines and enhanced pricing for other lines.

Bids that the PBC considers to be materially unbalanced will be rejected.

	T	,	1		,	
35	******	HOT-MIX ASPHALT SURFACE COURSE, PATCH, N70 (HAND METHOD)	Ton	0		
36	60600605	CONCRETE CURB, TYPE B	Foot	43		
37	*****	HIGH EARLY STRENGTH PORTLAND CEMENT CONCRETE COMBINATION CURB AND GUTTER, TYPE B-V.12	Foot	33		
38	CDOT 6060020	COMBINATION CONCRETE CURB AND GUTTER, TYPE B-V.12	Foot	4		
39	*****	MANHOLE, 3 FT DIAMETER, TYPE A, FRAME AND CLOSED LID (CITY OF CHICAGO)	Each	2		
40	*****	CATCH BASINS, TYPE A, SPECIAL, 3 FT DIAMETER, TYPE 1 FRAME, OPEN LID (CITY OF CHICAGO)	Each	3		
41	CDOT6020010	CATCH BASINS, TYPE A, 4 FT DIAMETER, TYPE 1 FRAME, OPEN LID (CITY OF CHICAGO)	Each	0		
42	******	DRAINAGE AND UTILITY STRUCTURES TO BE ADJUSTED	Each	0		
43	*****	VORTEX RESTRICTOR	Each	1		
44	*****	STORM SEWERS, EXTRA STRENGTH VITRIFIED CLAY PIPE, 8 IN	Foot	161		
45	*****	STORM SEWERS, DUCTILE IRON PIPE, 18 IN	Foot	0		
46	*****	STORM SEWERS, EXTRA STRENGTH VITRIFIED CLAY PIPE, 15 IN	Foot	147		
47	*****	STORM SEWERS, EXTRA STRENGTH VITRIFIED CLAY PIPE, 18 IN	Foot	276		
48	CDOT6050010	REMOVING MANHOLES	Each	0		
49	CDOT6050020	REMOVING CATCH BASINS	Each	0		
50	*****	SEWER CLEANING AND TELEVISING	Foot	583		
51	*****	CATCH BASINS, MANHOLES, WATER VALVES, ROUNDWAYS, AND INLETS TO BE CLEANED	Each	0		
52	60100085	GEOTECHNICAL FABRIC	Square Yard	0		

Date of Issue: March 28, 2024
PBC: C1607\_CDOT Capital Program - Alleys (Various Locations) Package 1\_Book 1 Instructions to Bidders

### CDOT Capital Program - Alleys (Various Locations): Package 1 LOCATION: W. WAVELAND AVE/ W. ADDISON ST/N. ALBANY AVE/N. TROY ST - Ward 33

#### PBC PROJECT NO.: 22356C

CDOT PROJECT NO.: B-3-356 - PBC CONTRACT C1607

Bidder's pricing for each line item should carry its share of the costs of work, plus its share of overhead and profit.

Bidders should avoid nominal pricing for some lines and enhanced pricing for other lines.

Bids that the PBC considers to be materially unbalanced will be rejected.

			Total 223	56C Waveland/Troy	
57	*****	REMOVE AND RELOCATE SIGN PANEL AND POLE ASSEMBLY	Each	0	
56	*****	PREMOLDED RUBBER SPEED HUMPS	Each	0	
55	*****	CONSTRUCTION SIGN	Square Foot	64	
54	*****	HYDRAULIC SEEDING	Square Yard	5	
53	CDOT2110010	PULVERIZED TOPSOIL MIX	Cubic Yard	2	

Date of Issue: March 28, 2024 25 of 70

#### SCHEDULE OF PRICES - 22356D

CDOT Capital Program - Alleys (Various Locations): Package 1
LOCATION: W. HOLLYWOOD AVE/W. OLIVE AVE/N. HERMITAGE AVE/N. ASHLAND AVE - Ward 40

PBC PROJECT NO.: 22356D

CDOT PROJECT NO.: B-3-356 - PBC CONTRACT C1605

Bidder's pricing for each line item should carry its share of the costs of work, plus its share of overhead and profit.

Bidders should avoid nominal pricing for some lines and enhanced pricing for other lines.

Bids that the PBC considers to be materially unbalanced will be rejected.

Line	Code Number	Description	Unit	Estimated Quantity	Unit Price	Cost
1	*****	EARTH EXCAVATION (SOIL TO CCDD FACILITY)	Cubic Yard	295		
2	*****	EARTH EXCAVATION (SOIL TO LANDFILL)	Cubic Yard	255		
3	44000100	PAVEMENT REMOVAL	Square Yard	32		
4	*****	DRIVEWAY AND ALLEY RETURN PAVEMENT REMOVAL	Square Yard	572		
5	44000300	CURB REMOVAL	Foot	131		
6	44000500	COMBINATION CURB AND GUTTER REMOVAL	Foot	140		
7	44000600	SIDEWALK REMOVAL	Square Foot	419		
8	CDOT4400020	ALLEY PAVEMENT REMOVAL	Square Yard	1584		
9	*****	GARAGE APRON REMOVAL	Square Foot	2356		
10	20700220	POROUS GRANULAR EMBANKMENT (CA-1)	Cubic Yard	0		
11	31101100	SUB-BASE GRANULAR MATERIAL, TYPE B	Cubic Yard	369		
12	20800150	TRENCH BACKFILL	Cubic Yard	0		
13	CDOT3110030	PERVIOUS AGGREGATE SUBBASE	Cubic Yard	0		
14	******	BEDDING & VOID OPENING AGGREGATES FOR PERMEABLE CONCRETE BLOCK PAVERS	Cubic Yard	0		
15	*****	CRUSHED STONE (TEMPORARY USE)	Ton	60		
16	35300200	PORTLAND CEMENT CONCRETE BASE COURSE, 7 IN	Square Yard	32		
17	35300400	PORTLAND CEMENT CONCRETE BASE COURSE, 9 IN	Square Yard	0		

Date of Issue: March 28, 2024
PBC: C1607\_CDOT Capital Program - Alleys (Various Locations) Package 1\_Book 1 Instructions to Bidders

# CDOT Capital Program - Alleys (Various Locations): Package 1 LOCATION: W. HOLLYWOOD AVE/W. OLIVE AVE/N. HERMITAGE AVE/N. ASHLAND AVE - Ward 40 PBC PROJECT NO.: 22356D

#### CDOT PROJECT NO.: B-3-356 - PBC CONTRACT C1605

Bidder's pricing for each line item should carry its share of the costs of work, plus its share of overhead and profit.

Bidders should avoid nominal pricing for some lines and enhanced pricing for other lines.

Bids that the PBC considers to be materially unbalanced will be rejected.

	,	•	1	
18	CDOT4230030	HIGH EARLY STRENGTH PORTLAND CEMENT CONCRETE ALLEY PAVEMENT, 8 INCH	Square Yard	1642
19	CDOT4230010	HIGH EARLY STRENGTH PORTLAND CEMENT CONCRETE DRIVEWAY PAVEMENT, 8 INCH	Square Yard	0
20	******	HIGH EARLY STRENGTH PORTLAND CEMENT CONCRETE GARAGE APRON, 8 INCH	Square Foot	2356
21	******	HIGH EARLY STRENGTH PORTLAND CEMENT CONCRETE SIDEWALK, 8 INCH	Square Foot	766
22	******	PORTLAND CEMENT CONCRETE SIDEWALK, 8 IN	Square Foot	0
23	*****	PORTLAND CEMENT CONCRETE SIDEWALK, 5 IN	Square Foot	231
24	******	PORTLAND CEMENT CONCRETE ADA CURB RAMP, 5 IN	Square Foot	188
25	******	HIGH EARLY STRENGTH PORTLAND CEMENT CONCRETE ADA CURB RAMP, 8 INCH	Square Foot	0
26	*****	DRILL AND GROUT DOWELS AND TIE BARS	Each	227
27	******	PORTLAND CEMENT CONCRETE COLLAR FOR PERMEABLE BLOCK PAVERS, POROUS TILE PAVERS, OR PERVIOUS HMA	Foot	0
28	*****	PERMEABLE CONCRETE BLOCK PAVERS	Square Foot	0
29	*****	GREEN ALLEY IDENTIFIER CONCRETE STAMP	Each	3
30	40600200	BITUMINOUS MATERIALS (TACK COAT)	Pound	15
31	4060105	HOT-MIX ASPHALT SURFACE COURSE, IL-9.5L, MIX "C", N30 (CDOT)	Ton	0
32	40603085	HOT-MIX ASPHALT BINDER COURSE, N70	Ton	0
33	*****	HOT-MIX ASPHALT, REMOVE AND RESURFACE, N30	Square Yard	0
34	******	HOT-MIX ASPHALT SURFACE COURSE, PATCH, N30 (HAND METHOD)	Ton	6

Date of Issue: March 28, 2024

# CDOT Capital Program - Alleys (Various Locations): Package 1 LOCATION: W. HOLLYWOOD AVE/W. OLIVE AVE/N. HERMITAGE AVE/N. ASHLAND AVE - Ward 40 PBC PROJECT NO.: 22356D

#### CDOT PROJECT NO.: B-3-356 - PBC CONTRACT C1605

Bidder's pricing for each line item should carry its share of the costs of work, plus its share of overhead and profit.

Bidders should avoid nominal pricing for some lines and enhanced pricing for other lines.

Bids that the PBC considers to be materially unbalanced will be rejected.

25	*****	LIGT MIV ACRUALT CUREAGE	T	^	
35		HOT-MIX ASPHALT SURFACE COURSE, PATCH, N70 (HAND	Ton	0	
		METHOD)			
36	60600605	CONCRETE CURB, TYPE B	Foot	131	
37	*****	HIGH EARLY STRENGTH PORTLAND	Foot	72	
		CEMENT CONCRETE COMBINATION			
20	CDOT C000000	CURB AND GUTTER, TYPE B-V.12	F4	00	
38	CDOT 6060020	COMBINATION CONCRETE CURB AND GUTTER, TYPE B-V.12	Foot	68	
39	*****	MANHOLE, 3 FT DIAMETER, TYPE A,	Each	0	
		FRAME AND CLOSED LID (CITY OF		•	
		CHICAGO)			
40	*****	CATCH BASINS, TYPE A, SPECIAL, 3	Each	0	
		FT DIAMETER, TYPE 1 FRAME, OPEN			
41	CDOT6020010	LID (CITY OF CHICAGO)  CATCH BASINS, TYPE A, 4 FT	Each	2	
71	00010020010	DIAMETER, TYPE 1 FRAME, OPEN LID	Lacii	2	
		(CITY OF CHICAGO)			
42	*****	DRAINAGE AND UTILITY	Each	6	
		STRUCTURES TO BE ADJUSTED			
43	*****	VORTEX RESTRICTOR	Each	0	
44	******	STORM SEWERS, EXTRA STRENGTH	Foot	0	
45	*****	VITRIFIED CLAY PIPE, 8 IN STORM SEWERS, DUCTILE IRON	Foot	0	
40		PIPE, 18 IN	<b>Γ</b> 00ι	U	
46	*****	STORM SEWERS, EXTRA STRENGTH	Foot	0	
		VITRIFIED CLAY PIPE, 15 IN			
47	******	STORM SEWERS, EXTRA STRENGTH	Foot	0	
		VITRIFIED CLAY PIPE, 18 IN			
48	CDOT6050010	REMOVING MANHOLES	Each	0	
49	CDOT6050020	REMOVING CATCH BASINS	Each	2	
50	******	SEWER CLEANING AND TELEVISING	Foot	192	
51	*****	CATCH BASINS, MANHOLES, WATER	Each	4	
		VALVES, ROUNDWAYS, AND INLETS			
52	60100085	TO BE CLEANED GEOTECHNICAL FABRIC	Square	0	
52	00100000	OLO I LOI INIOAL I ADINIO	Yard	U	
53	CDOT2110010	PULVERIZED TOPSOIL MIX	Cubic Yard	14	
54	*****	HYDRAULIC SEEDING	Square	25	
			Yard		

Date of Issue: March 28, 2024

# CDOT Capital Program - Alleys (Various Locations): Package 1 LOCATION: W. HOLLYWOOD AVE/W. OLIVE AVE/N. HERMITAGE AVE/N. ASHLAND AVE - Ward 40 PBC PROJECT NO.: 22356D

# CDOT PROJECT NO.: B-3-356 – PBC CONTRACT C1605

Bidder's pricing for each line item should carry its share of the costs of work, plus its share of overhead and profit.

Bidders should avoid nominal pricing for some lines and enhanced pricing for other lines.

Bids that the PBC considers to be materially unbalanced will be rejected.

55	*****	CONSTRUCTION SIGN	Square Foot	64		
56	*****	PREMOLDED RUBBER SPEED HUMPS	Each	2		
57	*****	REMOVE AND RELOCATE SIGN PANEL AND POLE ASSEMBLY	Each	0		
		Total 22356D Hollywood/Hermitage				

Date of Issue: March 28, 2024 29 of 70

#### **SCHEDULE OF PRICES – 22356E**

CDOT Capital Program - Alleys (Various Locations): Package 1

LOCATION: W. GLENLAKE AVENUE/W. PETERSON AVENUE/N. PAULINA ŚTREET/N. CLARK STREET - Ward 40 PBC PROJECT NO.: 22356E

CDOT PROJECT NO.: B-3-356 - PBC CONTRACT C1607

Bidder's pricing for each line item should carry its share of the costs of work, plus its share of overhead and profit.

Bidders should avoid nominal pricing for some lines and enhanced pricing for other lines.

Bids that the PBC considers to be materially unbalanced will be rejected.

Line	Code Number	Description	Unit	Estimated Quantity	Unit Price	Cost
1	*****	EARTH EXCAVATION (SOIL TO CCDD FACILITY)	Cubic Yard	0		
2	*****	EARTH EXCAVATION (SOIL TO LANDFILL)	Cubic Yard	205		
3	44000100	PAVEMENT REMOVAL	Square Yard	11		
4	******	DRIVEWAY AND ALLEY RETURN PAVEMENT REMOVAL	Square Yard	50		
5	44000300	CURB REMOVAL	Foot	35		
6	44000500	COMBINATION CURB AND GUTTER REMOVAL	Foot	50		
7	44000600	SIDEWALK REMOVAL	Square Foot	195		
8	CDOT4400020	ALLEY PAVEMENT REMOVAL	Square Yard	369		
9	*****	GARAGE APRON REMOVAL	Square Foot	142		
10	20700220	POROUS GRANULAR EMBANKMENT (CA-1)	Cubic Yard	40		
11	31101100	SUB-BASE GRANULAR MATERIAL, TYPE B	Cubic Yard	78		
12	20800150	TRENCH BACKFILL	Cubic Yard	14		
13	CDOT3110030	PERVIOUS AGGREGATE SUBBASE	Cubic Yard	32		
14	******	BEDDING & VOID OPENING AGGREGATES FOR PERMEABLE CONCRETE BLOCK PAVERS	Cubic Yard	7		
15	*****	CRUSHED STONE (TEMPORARY USE)	Ton	30		
16	35300200	PORTLAND CEMENT CONCRETE BASE COURSE, 7 IN	Square Yard	11		
17	35300400	PORTLAND CEMENT CONCRETE BASE COURSE, 9 IN	Square Yard	0		

Date of Issue: March 28, 2024

LOCATION: W. GLENLAKE AVENUE/W. PETERSON AVENUE/N. PAULINA STREET/N. CLARK STREET - Ward 40 PBC PROJECT NO.: 22356E

#### CDOT PROJECT NO.: B-3-356 - PBC CONTRACT C1607

Bidder's pricing for each line item should carry its share of the costs of work, plus its share of overhead and profit. Bidders should avoid nominal pricing for some lines and enhanced pricing for other lines. Bids that the PBC considers to be materially unbalanced will be rejected.

18	CDOT4230030	HIGH EARLY STRENGTH PORTLAND CEMENT CONCRETE ALLEY PAVEMENT, 8 INCH	Square Yard	150	
19	CDOT4230010	HIGH EARLY STRENGTH PORTLAND CEMENT CONCRETE DRIVEWAY PAVEMENT, 8 INCH	Square Yard	12	
20	******	HIGH EARLY STRENGTH PORTLAND CEMENT CONCRETE GARAGE APRON, 8 INCH	Square Foot	142	
21	******	HIGH EARLY STRENGTH PORTLAND CEMENT CONCRETE SIDEWALK, 8 INCH	Square Foot	92	
22	******	PORTLAND CEMENT CONCRETE SIDEWALK, 8 IN	Square Foot	0	
23	******	PORTLAND CEMENT CONCRETE SIDEWALK, 5 IN	Square Foot	163	
24	*****	PORTLAND CEMENT CONCRETE ADA CURB RAMP, 5 IN	Square Foot	32	
25	******	HIGH EARLY STRENGTH PORTLAND CEMENT CONCRETE ADA CURB RAMP, 8 INCH	Square Foot	22	
26	******	DRILL AND GROUT DOWELS AND TIE BARS	Each	21	
27	******	PORTLAND CEMENT CONCRETE COLLAR FOR PERMEABLE BLOCK PAVERS, POROUS TILE PAVERS, OR PERVIOUS HMA	Foot	420	
28	*****	PERMEABLE CONCRETE BLOCK PAVERS	Square Foot	1439	
29	*****	GREEN ALLEY IDENTIFIER CONCRETE STAMP	Each	2	
30	40600200	BITUMINOUS MATERIALS (TACK COAT)	Pound	6	
31	4060105	HOT-MIX ASPHALT SURFACE COURSE, IL-9.5L, MIX "C", N30 (CDOT)	Ton	0	
32	40603085	HOT-MIX ASPHALT BINDER COURSE, N70	Ton	0	
33	*****	HOT-MIX ASPHALT, REMOVE AND RESURFACE, N30	Square Yard	0	
34	******	HOT-MIX ASPHALT SURFACE COURSE, PATCH, N30 (HAND METHOD)	Ton	2	

LOCATION: W. GLENLAKE AVENUE/W. PETERSON AVENUE/N. PAULINA ŜTREET/N. CLARK STREET - Ward 40 PBC PROJECT NO.: 22356E

#### CDOT PROJECT NO.: B-3-356 - PBC CONTRACT C1607

Bidder's pricing for each line item should carry its share of the costs of work, plus its share of overhead and profit.

Bidders should avoid nominal pricing for some lines and enhanced pricing for other lines.

Bids that the PBC considers to be materially unbalanced will be rejected.

0.5	*****	LIGT MIN A OBLIALT OF SEC.	T -	10	1
35	******	HOT-MIX ASPHALT SURFACE	Ton	0	
		COURSE, PATCH, N70 (HAND METHOD)			
36	60600605	CONCRETE CURB, TYPE B	Foot	35	
37	*****	HIGH EARLY STRENGTH PORTLAND	Foot	36	
		CEMENT CONCRETE COMBINATION			
		CURB AND GUTTER, TYPE B-V.12			
38	CDOT 6060020	COMBINATION CONCRETE CURB AND GUTTER, TYPE B-V.12	Foot	14	
39	*****	MANHOLE, 3 FT DIAMETER, TYPE A,	Each	0	
00		FRAME AND CLOSED LID (CITY OF	Laoii		
		CHICAGO)			
40	*****	CATCH BASINS, TYPE A, SPECIAL, 3	Each	0	
		FT DIAMETER, TYPE 1 FRAME,			
		OPEN LID (CITY OF CHICAGO)			
41	CDOT6020010	CATCH BASINS, TYPE A, 4 FT	Each	0	
		DIAMETER, TYPE 1 FRAME, OPEN LID (CITY OF CHICAGO)			
42	*****	DRAINAGE AND UTILITY	Each	0	
42		STRUCTURES TO BE ADJUSTED	Lacii	0	
43	*****	VORTEX RESTRICTOR	Each	0	
44	*****	STORM SEWERS, EXTRA	Foot	0	
		STRENGTH VITRIFIED CLAY PIPE, 8			
		IN			
45	*****	STORM SEWERS, DUCTILE IRON	Foot	0	
10	*****	PIPE, 18 IN			
46	******	STORM SEWERS, EXTRA	Foot	0	
		STRENGTH VITRIFIED CLAY PIPE, 15 IN			
47	*****	STORM SEWERS, EXTRA	Foot	0	
71		STRENGTH VITRIFIED CLAY PIPE,	1 000		
		18 IN			
48	CDOT6050010	REMOVING MANHOLES	Each	0	
49	CDOT6050020	REMOVING CATCH BASINS	Each	0	
50	*****	SEWER CLEANING AND TELEVISING	Foot	0	
51	*****	CATCH BASINS, MANHOLES, WATER	Each	0	
		VALVES, ROUNDWAYS, AND INLETS			
	0040000	TO BE CLEANED		1011	
52	60100085	GEOTECHNICAL FABRIC	Square	314	
E2	CDOT2440040		Yard	2	
53	CDOT2110010	PULVERIZED TOPSOIL MIX	Cubic Yard	\ \ \ \ \ \ \ \ \ \ \ \ \ \ \ \ \ \ \	
			I alu		1

Date of Issue: March 28, 2024

LOCATION: W. GLENLAKE AVENUE/W. PETERSON AVENUE/N. PAULINA STREET/N. CLARK STREET - Ward 40 PBC PROJECT NO.: 22356E

#### CDOT PROJECT NO.: B-3-356 - PBC CONTRACT C1607

Bidder's pricing for each line item should carry its share of the costs of work, plus its share of overhead and profit.

Bidders should avoid nominal pricing for some lines and enhanced pricing for other lines.

Bids that the PBC considers to be materially unbalanced will be rejected.

			Total 22356E Glenlake/Paulina			\$0.00
57	*****	REMOVE AND RELOCATE SIGN PANEL AND POLE ASSEMBLY	Each	0		
56	*****	PREMOLDED RUBBER SPEED HUMPS	Each	0		
55	******	CONSTRUCTION SIGN	Square Foot	32		
54	*****	HYDRAULIC SEEDING	Square Yard	4		

Date of Issue: March 28, 2024

#### SCHEDULE OF PRICES - 22356GF

CDOT Capital Program - Alleys (Various Locations): Package 1 LOCATION: W. WILSON AVE/W. SUNNYSIDE AVE./N. SPAULDING AVE./N. SAWYER AVE. Ward 33

#### PBC PROJECT NO.: 22356F

CDOT PROJECT NO.: B-3-356 - PBC CONTRACT C1607

Bidder's pricing for each line item should carry its share of the costs of work, plus its share of overhead and profit. Bidders should avoid nominal pricing for some lines and enhanced pricing for other lines.

Bids that the PBC considers to be materially unbalanced will be rejected.

Line	Code Number	Description	Unit	Estimated Quantity	Unit Price	Cost
1	*****	EARTH EXCAVATION (SOIL TO CCDD FACILITY)	Cubic Yard	219		
2	*****	EARTH EXCAVATION (SOIL TO LANDFILL)	Cubic Yard	226		
3	44000100	PAVEMENT REMOVAL	Square Yard	24		
4	*****	DRIVEWAY AND ALLEY RETURN PAVEMENT REMOVAL	Square Yard	68		
5	44000300	CURB REMOVAL	Foot	115		
6	44000500	COMBINATION CURB AND GUTTER REMOVAL	Foot	86		
7	44000600	SIDEWALK REMOVAL	Square Foot	634		
8	CDOT4400020	ALLEY PAVEMENT REMOVAL	Square Yard	1203		
9	*****	GARAGE APRON REMOVAL	Square Foot	1741		
10	20700220	POROUS GRANULAR EMBANKMENT (CA-1)	Cubic Yard	0		
11	31101100	SUB-BASE GRANULAR MATERIAL, TYPE B	Cubic Yard	0		
12	20800150	TRENCH BACKFILL	Cubic Yard	280		
13	CDOT3110030	PERVIOUS AGGREGATE SUBBASE	Cubic Yard	0		
14	******	BEDDING & VOID OPENING AGGREGATES FOR PERMEABLE CONCRETE BLOCK PAVERS	Cubic Yard	0		
15	*****	CRUSHED STONE (TEMPORARY USE)	Ton	40		
16	35300200	PORTLAND CEMENT CONCRETE BASE COURSE, 7 IN	Square Yard	24		

Date of Issue: March 28, 2024 34 of 70

# CDOT Capital Program - Alleys (Various Locations): Package 1 LOCATION: W. WILSON AVE/W. SUNNYSIDE AVE./N. SPAULDING AVE./N. SAWYER AVE. Ward 33

# PBC PROJECT NO.: 22356F

CDOT PROJECT NO.: B-3-356 - PBC CONTRACT C1607

Bidder's pricing for each line item should carry its share of the costs of work, plus its share of overhead and profit. Bidders should avoid nominal pricing for some lines and enhanced pricing for other lines.

Bids that the PBC considers to be materially unbalanced will be rejected.

		s that the FDC considers to be materially	_	wiii be rejected.	
17	35300400	PORTLAND CEMENT CONCRETE	Square	0	
		BASE COURSE, 9 IN	Yard		
18	CDOT4230030	HIGH EARLY STRENGTH	Square	1246	
		PORTLAND CEMENT CONCRETE	Yard		
		ALLEY PAVEMENT, 8 INCH			
19	CDOT4230010	HIGH EARLY STRENGTH	Square	0	
		PORTLAND CEMENT CONCRETE	Yard		
		DRIVEWAY PAVEMENT, 8 INCH			
20	*****	HIGH EARLY STRENGTH	Square	1741	
		PORTLAND CEMENT CONCRETE	Foot		
		GARAGE APRON, 8 INCH			
21	*****	HIGH EARLY STRENGTH	Square	219	
		PORTLAND CEMENT CONCRETE	Foot		
		SIDEWALK, 8 INCH	1 001		
22	*****	PORTLAND CEMENT CONCRETE	Square	283	
		SIDEWALK, 8 IN	Foot		
23	*****	PORTLAND CEMENT CONCRETE	Square	213	
20		SIDEWALK, 5 IN	Foot	210	
24	*****	PORTLAND CEMENT CONCRETE	Square	139	
<del>24</del>		ADA CURB RAMP, 5 IN	Foot	100	
25	*****	HIGH EARLY STRENGTH	Square	0	
23		PORTLAND CEMENT CONCRETE	Foot		
			FOOL		
00	*****	ADA CURB RAMP, 8 INCH	Ta ala	475	
26		DRILL AND GROUT DOWELS AND	Each	175	
	*****	TIE BARS	<b>+_</b> .		
27	*****	PORTLAND CEMENT CONCRETE	Foot	0	
		COLLAR FOR PERMEABLE BLOCK			
		PAVERS, POROUS TILE PAVERS,			
		OR PERVIOUS HMA			
28	******	PERMEABLE CONCRETE BLOCK	Square	0	
		PAVERS	Foot		
29	*****	GREEN ALLEY IDENTIFIER	Each	3	
		CONCRETE STAMP	<u> </u>		
30	40600200	BITUMINOUS MATERIALS (TACK	Pound	9	
		COAT)			
31	4060105	HOT-MIX ASPHALT SURFACE	Ton	0	
		COURSE, IL-9.5L, MIX "C", N30			
		(CDOT)			
32	40603085	HOT-MIX ASPHALT BINDER	Ton	0	
			1		

Date of Issue: March 28, 2024

35 of 70

# CDOT Capital Program - Alleys (Various Locations): Package 1 LOCATION: W. WILSON AVE/W. SUNNYSIDE AVE./N. SPAULDING AVE./N. SAWYER AVE. Ward 33

# PBC PROJECT NO.: 22356F

CDOT PROJECT NO.: B-3-356 - PBC CONTRACT C1607

Bidder's pricing for each line item should carry its share of the costs of work, plus its share of overhead and profit.

Bidders should avoid nominal pricing for some lines and enhanced pricing for other lines.

Bids that the PBC considers to be materially unbalanced will be rejected.

33	*******	S that the PBC considers to be materially			1. T	
33		HOT-MIX ASPHALT, REMOVE AND RESURFACE, N30	Square Yard	0		
34	*****	HOT-MIX ASPHALT SURFACE COURSE, PATCH, N30 (HAND METHOD)	Ton	5		
35	*****	HOT-MIX ASPHALT SURFACE COURSE, PATCH, N70 (HAND METHOD)	Ton	0		
36	60600605	CONCRETE CURB, TYPE B	Foot	115		
37	*****	HIGH EARLY STRENGTH PORTLAND CEMENT CONCRETE COMBINATION CURB AND GUTTER, TYPE B-V.12	Foot	50		
38	CDOT 6060020	COMBINATION CONCRETE CURB AND GUTTER, TYPE B-V.12	Foot	36		
39	*****	MANHOLE, 3 FT DIAMETER, TYPE A, FRAME AND CLOSED LID (CITY OF CHICAGO)	Each	0		
40	*****	CATCH BASINS, TYPE A, SPECIAL, 3 FT DIAMETER, TYPE 1 FRAME, OPEN LID (CITY OF CHICAGO)	Each	0		
41	CDOT6020010	CATCH BASINS, TYPE A, 4 FT DIAMETER, TYPE 1 FRAME, OPEN LID (CITY OF CHICAGO)	Each	0		
42	******	DRAINAGE AND UTILITY STRUCTURES TO BE ADJUSTED	Each	1		
43	*****	VORTEX RESTRICTOR	Each	0		
44	*****	STORM SEWERS, EXTRA STRENGTH VITRIFIED CLAY PIPE, 8 IN	Foot	0		
45	*****	STORM SEWERS, DUCTILE IRON PIPE, 18 IN	Foot	0		
46	*****	STORM SEWERS, EXTRA STRENGTH VITRIFIED CLAY PIPE, 15 IN	Foot	0		
47	*****	STORM SEWERS, EXTRA STRENGTH VITRIFIED CLAY PIPE, 18 IN	Foot	0		
48	CDOT6050010	REMOVING MANHOLES	Each	0		

Date of Issue: March 28, 2024

36 of 70

# CDOT Capital Program - Alleys (Various Locations): Package 1 LOCATION: W. WILSON AVE/W. SUNNYSIDE AVE./N. SPAULDING AVE./N. SAWYER AVE. Ward 33

# vvard 33

# PBC PROJECT NO.: 22356F CDOT PROJECT NO.: B-3-356 – PBC CONTRACT C1607

Bidder's pricing for each line item should carry its share of the costs of work, plus its share of overhead and profit.

Bidders should avoid nominal pricing for some lines and enhanced pricing for other lines.

Bids that the PBC considers to be materially unbalanced will be rejected.

49	CDOT6050020	REMOVING CATCH BASINS	Each	0	
50	*****	SEWER CLEANING AND TELEVISING	Foot	0	
51	******	CATCH BASINS, MANHOLES, WATER VALVES, ROUNDWAYS, AND INLETS TO BE CLEANED	Each	0	
52	60100085	GEOTECHNICAL FABRIC	Square Yard	0	
53	CDOT2110010	PULVERIZED TOPSOIL MIX	Cubic Yard	10	
54	*****	HYDRAULIC SEEDING	Square Yard	17	
55	*****	CONSTRUCTION SIGN	Square Foot	64	
56	*****	PREMOLDED RUBBER SPEED HUMPS	Each	0	
57	******	REMOVE AND RELOCATE SIGN PANEL AND POLE ASSEMBLY	Each	0	
			Total 22356F Wilson/Sunnyside		

Date of Issue: March 28, 2024 37 of 70

# **SCHEDULE OF PRICES - 22356G**

CDOT Capital Program - Alleys (Various Locations): Package 1
LOCATION: W. NORTH SHORE AVE/W. ALBION AVE/N. ARTESIAN AVE/N. WESTERN AVE. - Ward 50
PBC PROJECT NO.: 22356G

CDOT PROJECT NO.: B-3-356 - PBC CONTRACT C1607

Bidder's pricing for each line item should carry its share of the costs of work, plus its share of overhead and profit.

Bidders should avoid nominal pricing for some lines and enhanced pricing for other lines.

Bids that the PBC considers to be materially unbalanced will be rejected.

Line	Code Number	Description	Unit	Estimated	Unit	Cost
				Quantity	Price	
4	*****	EARTH EVON ATION (OOL TO	01: 1/	50		
1		EARTH EXCAVATION (SOIL TO CCDD FACILITY)	Cubic Yard	53		
2	*****	EARTH EXCAVATION (SOIL TO LANDFILL)	Cubic Yard	335		
3	44000100	PAVEMENT REMOVAL	Square Yard	21		
4	*****	DRIVEWAY AND ALLEY RETURN PAVEMENT REMOVAL	Square Yard	90		
5	44000300	CURB REMOVAL	Foot	93		
6	44000500	COMBINATION CURB AND GUTTER REMOVAL	Foot	94		
7	44000600	SIDEWALK REMOVAL	Square Foot	327		
8	CDOT4400020	ALLEY PAVEMENT REMOVAL	Square Yard	1068		
9	*****	GARAGE APRON REMOVAL	Square Foot	1159		
10	20700220	POROUS GRANULAR EMBANKMENT (CA-1)	Cubic Yard	0		
11	31101100	SUB-BASE GRANULAR MATERIAL, TYPE B	Cubic Yard	252		
12	20800150	TRENCH BACKFILL	Cubic Yard	115		
13	CDOT3110030	PERVIOUS AGGREGATE SUBBASE	Cubic Yard	0		
14	*****	BEDDING & VOID OPENING AGGREGATES FOR PERMEABLE CONCRETE BLOCK PAVERS	Cubic Yard	0		
15	*****	CRUSHED STONE (TEMPORARY USE)	Ton	50		
16	35300200	PORTLAND CEMENT CONCRETE BASE COURSE, 7 IN	Square Yard	21		
17	35300400	PORTLAND CEMENT CONCRETE BASE COURSE, 9 IN	Square Yard	0		

38 of 70

Date of Issue: March 28, 2024

# CDOT Capital Program - Alleys (Various Locations): Package 1

LOCATION: W. NORTH SHORE AVE/W. ALBION AVE/N. ARTESIAN AVE/N. WESTERN AVE. - Ward 50

# PBC PROJECT NO.: 22356G

CDOT PROJECT NO.: B-3-356 - PBC CONTRACT C1607

Bidder's pricing for each line item should carry its share of the costs of work, plus its share of overhead and profit.

Bidders should avoid nominal pricing for some lines and enhanced pricing for other lines.

Bids that the PBC considers to be materially unbalanced will be rejected.

		that the r be considere to be materially	aribalariooa	mii bo rojootoa.	 
18	CDOT4230030	HIGH EARLY STRENGTH PORTLAND CEMENT CONCRETE ALLEY PAVEMENT, 8 INCH	Square Yard	1108	
19	CDOT4230010	HIGH EARLY STRENGTH PORTLAND CEMENT CONCRETE DRIVEWAY PAVEMENT, 8 INCH	Square Yard	17	
20	*****	HIGH EARLY STRENGTH PORTLAND CEMENT CONCRETE GARAGE APRON, 8 INCH	Square Foot	1159	
21	*****	HIGH EARLY STRENGTH PORTLAND CEMENT CONCRETE SIDEWALK, 8 INCH	Square Foot	266	
22	******	PORTLAND CEMENT CONCRETE SIDEWALK, 8 IN	Square Foot	0	
23	******	PORTLAND CEMENT CONCRETE SIDEWALK, 5 IN	Square Foot	237	
24	******	PORTLAND CEMENT CONCRETE ADA CURB RAMP, 5 IN	Square Foot	90	
25	*****	HIGH EARLY STRENGTH PORTLAND CEMENT CONCRETE ADA CURB RAMP, 8 INCH	Square Foot	31	
26	*****	DRILL AND GROUT DOWELS AND TIE BARS	Each	158	
27	******	PORTLAND CEMENT CONCRETE COLLAR FOR PERMEABLE BLOCK PAVERS, POROUS TILE PAVERS, OR PERVIOUS HMA	Foot	0	
28	******	PERMEABLE CONCRETE BLOCK PAVERS	Square Foot	0	
29	******	GREEN ALLEY IDENTIFIER CONCRETE STAMP	Each	2	
30	40600200	BITUMINOUS MATERIALS (TACK COAT)	Pound	10	
31	4060105	HOT-MIX ASPHALT SURFACE COURSE, IL-9.5L, MIX "C", N30 (CDOT)	Ton	0	
32	40603085	HOT-MIX ASPHALT BINDER COURSE, N70	Ton	0	
33	******	HOT-MIX ASPHALT, REMOVE AND RESURFACE, N30	Square Yard	0	

Date of Issue: March 28, 2024 39 of 70

# CDOT Capital Program - Alleys (Various Locations): Package 1

LOCATION: W. NORTH SHORE AVE/W. ALBION AVE/N. ARTESIAN AVE/N. WESTERN AVE. - Ward 50

# PBC PROJECT NO.: 22356G

CDOT PROJECT NO.: B-3-356 - PBC CONTRACT C1607

Bidder's pricing for each line item should carry its share of the costs of work, plus its share of overhead and profit.

Bidders should avoid nominal pricing for some lines and enhanced pricing for other lines.

Bids that the PBC considers to be materially unbalanced will be rejected.

Dius	s that the PBC considers to be materially	unbalancec	a will be reject	leu.	
*****	HOT-MIX ASPHALT SURFACE COURSE, PATCH, N30 (HAND METHOD)	Ton	4		
*****	HOT-MIX ASPHALT SURFACE COURSE, PATCH, N70 (HAND METHOD)	Ton	0		
60600605	CONCRETE CURB, TYPE B	Foot	93		
*****	HIGH EARLY STRENGTH PORTLAND CEMENT CONCRETE COMBINATION CURB AND GUTTER, TYPE B-V.12	Foot	73		
CDOT 6060020	COMBINATION CONCRETE CURB AND GUTTER, TYPE B-V.12	Foot	22		
*****	MANHOLE, 3 FT DIAMETER, TYPE A, FRAME AND CLOSED LID (CITY OF CHICAGO)	Each	0		
*****	CATCH BASINS, TYPE A, SPECIAL, 3 FT DIAMETER, TYPE 1 FRAME, OPEN LID (CITY OF CHICAGO)	Each	0		
CDOT6020010	CATCH BASINS, TYPE A, 4 FT DIAMETER, TYPE 1 FRAME, OPEN LID (CITY OF CHICAGO)	Each	2		
******	DRAINAGE AND UTILITY STRUCTURES TO BE ADJUSTED	Each	2		
******	VORTEX RESTRICTOR	Each	1		
*****	STORM SEWERS, EXTRA STRENGTH VITRIFIED CLAY PIPE, 8 IN	Foot	109		
******	STORM SEWERS, DUCTILE IRON PIPE, 18 IN	Foot	226		
*****	STORM SEWERS, EXTRA STRENGTH VITRIFIED CLAY PIPE, 15 IN	Foot	0		
*****	STORM SEWERS, EXTRA STRENGTH VITRIFIED CLAY PIPE, 18 IN	Foot	0		
CDOT6050010	REMOVING MANHOLES	Each	1		
CDOT6050020	REMOVING CATCH BASINS	Each	0		
******	SEWER CLEANING AND TELEVISING	Foot	109		
	*******  *******  60600605  *******  CDOT 6060020  *******  ******  *******  *******  ****	*********  HOT-MIX ASPHALT SURFACE COURSE, PATCH, N30 (HAND METHOD)  *********  HOT-MIX ASPHALT SURFACE COURSE, PATCH, N70 (HAND METHOD)  60600605  CONCRETE CURB, TYPE B  *********  HIGH EARLY STRENGTH PORTLAND CEMENT CONCRETE COMBINATION CURB AND GUTTER, TYPE B-V.12  CDOT 6060020  COMBINATION CONCRETE CURB AND GUTTER, TYPE B-V.12  ********  MANHOLE, 3 FT DIAMETER, TYPE A, FRAME AND CLOSED LID (CITY OF CHICAGO)  ********  CATCH BASINS, TYPE A, SPECIAL, 3 FT DIAMETER, TYPE 1 FRAME, OPEN LID (CITY OF CHICAGO)  CATCH BASINS, TYPE 1 FRAME, OPEN LID (CITY OF CHICAGO)  ********  DRAINAGE AND UTILITY STRUCTURES TO BE ADJUSTED  ********  VORTEX RESTRICTOR  ********  STORM SEWERS, EXTRA STRENGTH VITRIFIED CLAY PIPE, 8 IN  ********  STORM SEWERS, EXTRA STRENGTH VITRIFIED CLAY PIPE, 15 IN  ********  STORM SEWERS, EXTRA STRENGTH VITRIFIED CLAY PIPE, 15 IN  ********  STORM SEWERS, EXTRA STRENGTH VITRIFIED CLAY PIPE, 18 IN  ********  STORM SEWERS, EXTRA STRENGTH VITRIFIED CLAY PIPE, 18 IN  ********  STORM SEWERS, EXTRA STRENGTH VITRIFIED CLAY PIPE, 18 IN  ********  STORM SEWERS, EXTRA STRENGTH VITRIFIED CLAY PIPE, 18 IN  ********  STORM SEWERS, EXTRA STRENGTH VITRIFIED CLAY PIPE, 18 IN  CDOT6050010  REMOVING MANHOLES  CDOT6050020  REMOVING CATCH BASINS  *********  SEWER CLEANING AND	**************************************	HOT-MIX ASPHALT SURFACE	TOT-IMIX ASPITALT SURFACE   COURSE, PATCH, N30 (HAND METHOD)

Date of Issue: March 28, 2024 40 of 70

# CDOT Capital Program - Alleys (Various Locations): Package 1

LOCATION: W. NORTH SHORE AVE/W. ALBION AVE/N. ARTESIAN AVE/N. WESTERN AVE. - Ward 50

# PBC PROJECT NO.: 22356G

CDOT PROJECT NO.: B-3-356 - PBC CONTRACT C1607

Bidder's pricing for each line item should carry its share of the costs of work, plus its share of overhead and profit.

Bidders should avoid nominal pricing for some lines and enhanced pricing for other lines.

Bids that the PBC considers to be materially unbalanced will be rejected.

51	*****	CATCH BASINS, MANHOLES, WATER VALVES, ROUNDWAYS, AND INLETS TO BE CLEANED	Each	0	
52	60100085	GEOTECHNICAL FABRIC	Square Yard	0	
53	CDOT2110010	PULVERIZED TOPSOIL MIX	Cubic Yard	6	
54	*****	HYDRAULIC SEEDING	Square Yard	10	
55	******	CONSTRUCTION SIGN	Square Foot	64	
56	******	PREMOLDED RUBBER SPEED HUMPS	Each	3	
57	*****	REMOVE AND RELOCATE SIGN PANEL AND POLE ASSEMBLY	Each	0	
			Total 223560	 6 North Shore/Artesian	

The Schedule of Prices must be completed by the bidder <u>and</u> submitted with the bid package. Bidder's pricing for each line item should carry its share of the costs of work, plus its share of overhead and profit. Bidders should avoid nominal pricing for some lines and enhanced pricing for other lines. Bids that the PBC considers to be unbalanced will be rejected.

Bidders must utilize the amounts in the Schedule of Prices to calculate their Base Work Only bid (Bid Form Line 1).

REMAINDER OF PAGE LEFT BLANK INTENTIONALLY

Date of Issue: March 28, 2024 41 of 70

# E. ADDITIONAL ALLOWANCE SCHEDULES

This Project includes the following allowances:

1. Site Work Allowance in the amount of \$175,000.00 (prorated per Alley)

All Work shall be approved in writing by the Commission Representative prior to proceeding.

All unused portions of the allowance funds must be returned to the Commission.

# F. ALTERNATES

{INTENTIONALLY OMMITTED}

Remainder of Page Left Blank Intentionally

Date of Issue: March 28, 2024 42 of 70

# G. ACCEPTANCE OF THE BID IN WITNESS WHEREOF, the parties hereto have caused this instrument to be executed in two (2) original counterparts the \_\_\_\_\_ day of \_\_\_\_\_\_, in the year \_\_\_\_\_. (Board Date) PUBLIC BUILDING COMMISSION OF CHICAGO Mary Pat Witry, Secretary Mayor Brandon Johnson, Chairman **CONTRACTING PARTY** Contractor Name Address IF A CORPORATION: Name: Title: Signature: ATTEST BY: Secretary IF A PARTNERSHIP: Partner (Signature) Address Partner (Signature) Address Partner (Signature) Address IF A SOLE PROPRIETORSHIP: Signature Address **NOTARY PUBLIC** County of \_\_\_\_\_ State of \_\_\_\_ Subscribed and sworn to before me on this day of , 20 . Notary Public Signature Commission Expires: APPROVED AS TO FORM AND LEGALITY \_\_\_\_\_ Date: \_\_\_\_\_ Neal & Leroy, LLC

### V. BID SUPPORT DOCUMENTS

# A. Basis of Award (Award Criteria Figure) - USE EXCEL SHEET FOR SUBMISSION

To promote the intended goal of economic opportunity and maximize the use of minority personnel on this project, the Public Building Commission of Chicago has established the Award Criteria Figure formula for the purpose of evaluating bids and awarding the contract. A contract in the amount of the Total Base Bid (or Base Contract Price) will be awarded to the responsible bidder with the lowest Award Criteria Figure pursuant to Section III. P Basis of Award above. The Public Building Commission of Chicago reserves the right to check all calculations for accuracy. The fulfillment of the Award Criteria does not abrogate the responsibilities of the Contractor to comply with federal and state requirements under the Equal Employment Act and the Illinois Human Rights Act.

#### 1. Instructions

The Bidder shall complete an Award Criteria Figure Formula for both Total Base Bid and Total Base Bid with Alternate Scenario(s) and transfer the final Award Criteria Figure - Line 15 (of chart below) to the space provided on the itemized BID FORM. Failure to complete the formula may be cause for rejection of the Bidder's BID. The successful bidder will be held responsible for adhering to the figures submitted in Lines 1, 2, 4, 6, 8, 10 and 12 during construction of the project.

Lines 2, 4 and 6 in the formula shall not be greater than seventy percent (70%) in each category for the sole purpose of determining award of the contract. Similarly, lines 8, 10 and 12 shall not be greater than fifteen percent (15%) in each category for the purpose of award criteria only. The seventy percent (70%) and fifteen percent (15%) goals are not intended to restrict the total number of minority and female employees to be used on the project, but only to establish limiting figures for use in the formula.

### 2. Award Criteria Figure Formula

Line 1.	TOTAL BASE BID (Refer to Line 6 of BID FORM), in figures	
Line 2.	Percentage of the Journeyworkers hours that the Contractor proposes to be worked by minority Journey workers during construction of the project. (Maximum figure 0.70)	
Line 3.	Multiply Line 2 by Line 1 by 0.04	
Line 4.	Percentage of total Apprentice hours that the Contractor proposes to be worked by minority Apprentices during construction of the project. (Maximum figure 0.70)	
Line 5.	Multiply Line 4 by Line 1 by 0.03	
Line 6.	Percentage of the total Laborer hours that the Contractor proposes to be worked by minority Laborers during construction of the project. (Maximum figure 0.70)	
Line 7.	Multiply Line 6 by Line 1 by 0.01	
Line 8.	Percentage of total Journeyworker hours that the Contractor proposes to be worked by female Journeyworkers during the construction of the project. (Maximum figure 0.15)	
Line 9.	Multiply Line 8 by Line 1 by 0.04	

Date of Issue: March 28, 2024 44 of 70

Line 10.	Percentage of total Apprentice hours that the Contractor proposes to be worked by female Apprentices during construction of the project. (Maximum figure 0.15)	
Line 11.	Multiply Line 10 by Line 1 by 0.03	
Line 12.	Percentage of the total Laborer hours that the Contractor proposes to be worked by female Laborers during construction of the project. (Maximum figure 0.15)	
Line 13.	Multiply Line 12 by Line 1 by 0.01	
Line 14.	Summation of Lines 3, 5, 7, 9, 11, and 13	
Line 15.	Subtract Line 14 from Line 1 (= "Award Criteria Figure")	
	Award Criteria Figure (Insert Line 15 of Award Criteria Formula): \$	

# 3. Community Hiring Bonuses

In order to encourage maximum employment of interested and available residents of the project community on this project, the following bonus calculations shall apply:

- a. In calculating the hours worked by minority and women Journeyworkers, apprentices, and laborers under the Award Criteria Figure set out in Part V.A. "Basis of Award (Award Criteria Figure)," all hours worked by minority and women Journeyworkers, existing apprentices, and laborers who are residents of the project community shall be multiplied by 1.5.
- b. In calculating the hours worked by minority and women apprentices under the Award Criteria Figure set out in Part V "Bid Support Documents," all hours worked in new apprenticeships by minority and women apprentices who are residents of the project community shall be multiplied by 2.0.

## **Definitions**

"City of Chicago Residents" means persons domiciled within the City of Chicago. Salaried superintendents are excluded from coverage in this section. Domicile is an individual's one and only true, fixed, and permanent home and principal establishment.

"Project Community Residents" means persons domiciled within the "Project Community" as defined in Section II, A.6 above.

"New Apprenticeship" shall mean an apprenticeship begun for a person who has not held an apprenticeship card within ninety (90) days prior to beginning the project.

# 4. Liquidated Damages

The Contractor hereby consents and agrees that, in the event that it fails to comply with each of the minimum commitments submitted with this Bid on Lines 2, 4, 6, 8, 10, and 12 of the Award Criteria Figure formula, covering minority and female Journeyworkers, apprentices, and laborers respectively, the following shall apply.

If the total hours in any category for which a percentage is assigned in Lines 2, 4, 6, 8, 10, or 12 of the Award Criteria equals zero at the completion of the work, then a net deficiency of the entire percentage assigned will be deemed to exist. For any net deficiency in each category, the following amounts shall be deducted as liquidated damages from monies due the Contractor and the Contract Sum modified accordingly:

 For each full one (1%) percent deficiency of minority Journeyworkers not utilized – four cents per each hundred dollars of the base bid calculated as follows:

Each one (1%) percent deficiency toward the goal for female Journeyworkers (Line 8) shall be calculated in the same way.

Date of Issue: March 28, 2024 45 of 70

b. For each full one (1%) percent deficiency of minority apprentices not utilized – three cents per hundred dollars of the base bid calculated as follows:

Each one (1%) percent deficiency toward the goal for female apprentices (Line 10) shall be calculated in the same way.

c. For each one (1%) percent deficiency of minority laborers not utilized – one cent per each hundred dollars of the base bid calculated as follows:

Each one (1%) percent deficiency toward the goal for female laborers (Line 12) shall be calculated in the same way.

- d. Liquidated damages, if any, will be calculated for the first pay requests reflecting fifty percent (50%) completion, seventy-five percent (75%) completion, and ninety percent (90%) completion, respectively, based upon the Contractor's pay request together with all attendant certified payrolls and other required documentation of minority and women employment. The accrued liquidated damages and interest will be added to the retention provided elsewhere in this contract. The amount of liquidated damages due to the Commission under this provision will bear compound interest at the rate of 5% per annum, compounded monthly from the date of the Notice to Proceed to the date of approval of a deductive change order for liquidated damages. Should the total amount of liquidated damages due under all provisions of this contract exceed the amount of the Commission's retainage, compound interest on the amount over and above the retainage will continue to accrue until the entire amount of liquidated damages and compound interest is paid to the Commission.
- e. The Commission is aware that certain subcontract agreements under this contract may require subcontractors to contribute to payment of liquidated damages assessed under this provision. Should enforcement of subcontract liquidated damages provisions result in an aggregate total of subcontractor liquidated damages greater than the liquidated damages assessed hereunder against Contractor, then Contractor must pay the excess pro rata as a bonus to each subcontractor exceeding its subcontract commitments for minority or women employment, or both.

### 5. Reporting

In accordance with this commitment, the Contractor must submit both the Contractor's Payroll Record Form and the Contractor's Recapitulation of Minority and Female Worker Hours and Percentages Form on a monthly basis. All Subcontractors shall be listed on the Contractor's Recapitulation Form whether active or not. For the purpose of this report, the following group categories will be used:

- a. The classification "White" includes person of Indo-European descent.
- b. The classification "Black" or "African-American" includes persons having origins in any of the black racial groups of Africa.
- c. The classification "Hispanic" includes persons whose origins are from Mexico, Puerto Rico, Cuba, Central or South America, the Caribbean Islands or other Spanish culture or origin, regardless of race.
- The classification "Native American" includes persons who are Native Americans by virtue of tribal association.
- e. The classification "Asian-Pacific" includes persons whose origins are from East Asia, Southeast Asia, the Pacific Islands or the Indian sub-continent.
- f. The classification "Other" includes qualified individuals with disabilities who meet legitimate skill, experience, education or other requirements of employment positions held or sought and who perform the essential function with or without reasonable accommodation and other groups or other individuals found by the Public Building Commission of Chicago to be socially and economically disadvantaged and to have suffered actual racial or ethnic discrimination and decreased opportunities to compete in Chicago area markets.

Date of Issue: March 28, 2024 46 of 70

# 6. Major Trades

LandscapingExcavationCarpentryRoad MarkingsConcreteAsphaltElectricalPlumbing

For approval of other trades for consideration in the Award Criteria Figure formula, written approval should be requested from the Commission.

# 7. Trade Participation - For Information Only

The following information must be supplied by the Contractor for the purposes of evaluating figures supplied in the Award Criteria Figure formula. It is understood that these figures are estimates only and are not to be considered as limiting in any manner actual participation on the project.

Anticipated levels of minority participation, to be expressed as percentages, must be supplied for each trade, whether attributable to the Contractor's work force or any Subcontractor which will be active on this project.

TRADE PARTICIPATION	PERCENT OF MINORITY

Date of Issue: March 28, 2024 47 of 70

# VI. ADDITIONAL DOCUMENTS TO BE EXECUTED

# **Affidavit of Non-collusion**

STA	ATE OF ILLINOIS } }SS
СО	UNTY OF COOK }
	, being first duly sworn, deposes and says that:
(1)	He/She is
	(Owner, Partner, Officer, Representative or Agent) of
	the Bidder that has submitted the attached Bid;
(2)	That Bidder is fully informed respecting the preparation and contents of the attached Bid and of all pertinent circumstances respecting such Bid;
(3)	Such Bid is genuine and is not a collusive or sham bid;
(4)	Neither Bidder nor any of its officers, partners, owners, agents, representatives, employees, or parties in interest, including this affiant, has in any way colluded, connived, conspired, or agreed, directly or indirectly, with any other Bidder, firm, or person to submit a collusive or sham bid in connection with the Contract for which the attached bid has been submitted or to refrain from bidding in connection with such Contract, or has in any manner, directly or indirectly, sought by agreement or collusion or communication or conference with any other Bidder, firm, or person to fix the price or prices in the attached bid or in that of any other Bidder, or to fix any overhead, profit, or cost element of the bid price of any other Bidder, or to secure through any collusion, conspiracy, connivance or unlawful agreement any advantage against the Public Building Commission of Chicago or any person interested in the proposed Contract; and
(5)	The price or prices quoted in the attached Bid are fair and proper and are not tainted by any collusion, conspiracy, connivance, or unlawful agreement on the part of the Bidder or any of its agents, representatives, owners, employees, or parties in interest, including this affiant.
(6)	The Bidder is not barred from bidding as a result of having violated Illinois Criminal Code, 720 ILCS 5/33E-3 (Bidrigging), 720 ILCS 5/33E-4 (Bid rotating) or the Prevailing Wage Act, 30 ILCS 570/0.01 through 570/7.
(Sig	gned)
(Titl	le) scribed and sworn to before me this day of 20
(Titl	le) Commission expires:

Date of Issue: March 28, 2024 48 of 70

# **SCHEDULE B - Joint Venture Affidavit (1 of 3)**

This form is not required if all joint venturers are MBE/Non-MBE or WBE/Non-WBE firms. In such case, however, a written joint venture agreement among the MBE/Non-MBE or WBE/Non-WBE firms should be submitted. Each MBE/WBE joint venturer must also attach a copy of their current certification letter.

A.	Nar	ne of joint venture							
B.	Ado	Iress of joint venture							
C.	Pho	one number of joint venture							
D.	Ide	Identify the firms that comprise the joint venture							
	1.	Describe the role(s) of the MBE/WBE firm(s) in the joint venture. (Note that a "clearly defined portion of work" must here be shown as under the responsibility of the MBE/WBE firm.)							
	2.	Describe very briefly the experience and business qualifications of each non-MBE/WBE joint venturer.							
E.	Nat	ure of joint venture's business							
F.	Pro	vide a copy of the joint venture agreement.							
G.	Ow	nership: What percentage of the joint venture is claimed to be owned by MBE/WBE?%							
Н.	Spe	ecify as to:							
	1.	Profit and loss sharing%							
	2.	Capital contributions, including equipment%							
	3.	Other applicable ownership interests, including ownership options or other agreements which restrict ownership or control.							

# **SCHEDULE B - Joint Venture Affidavit (2 of 3)**

wh	o are	of and participation in this Contract: Identify by name, race, sex, and "firm" those ind responsible for day-to-day management and policy decision making, including, but responsibility for:	
1.	Fin	ancial decisions	
2.	Ма	nagement decisions such as:	
	a.	Estimating	
	b.	Marketing and Sales	
	C.	Hiring and firing of management personnel	
	d.	Other	
3.	Pur	rchasing of major items or supplies	
4.	Sup	pervision of field operations	
5.	Sup	pervision of office personnel	
6.	will	scribe the financial controls of the joint venture, e.g., will a separate cost center be estable for keeping the books; how will the expense therefor be reimbursed; the turer to commit or obligate the other. Describe the estimated contract cash flow for each	ne authority of each join
7.		ate approximate number of operational personnel, their craft and positions, and whethen the majority firm or the joint venture.	r they will be employees
Ple	ease s	state any material facts of additional information pertinent to the control and structure of	this joint venture.

# SCHEDULE B - Joint Venture Affidavit (3 of 3)

THE UNDERSIGNED SWEAR THAT THE FOREGOING STATEMENTS ARE CORRECT AND INCLUDE ALL MATERIAL INFORMATION NECESSARY TO IDENTIFY AND EXPLAIN THE TERMS AND OPERATIONS OF OUR JOINT VENTURE AND THE INTENDED PARTICIPATION BY EACH JOINT VENTURER IN THE UNDERTAKING. FURTHER, THE UNDERSIGNED COVENANT AND AGREE TO PROVIDE TO THE PUBLIC BUILDING COMMISSION OF CHICAGO CURRENT, COMPLETE AND ACCURATE INFORMATION REGARDING ACTUAL JOINT VENTURE WORK AND THE PAYMENT THEREFOR AND ANY PROPOSED CHANGES IN ANY OF THE JOINT VENTURE AGREEMENTS AND TO PERMIT THE AUDIT AND EXAMINATION OF THE BOOKS, RECORDS, AND FILES OF THE JOINT VENTURE, OR THOSE OF EACH JOINT VENTURER RELEVANT TO THE JOINT VENTURE, BY AUTHORIZED REPRESENTATIVES OF THE COMMISSION. ANY MATERIAL MISREPRESENTATION WILL BE GROUNDS FOR TERMINATING ANY CONTRACT WHICH MAY BE AWARDED AND FOR INITIATING ACTION UNDER FEDERAL OR STATE LAWS CONCERNING FALSE STATEMENTS.

Note: If, after filing this Schedule B and before the completion of the joint venture's work on this Contract, there is any significant change in the information submitted, the joint venture must inform the Public Building Commission of Chicago, either directly or through the General contractor if the joint venture is a subcontractor.

Name of Joint Venturer	Name of Joint Venturer
Signature	Signature
Name	Name
Title	Title
Date	Date
State ofCounty of	State of County of
On this, 20	On this day of, 20
before me appeared (Name)	before me appeared (Name)
to me personally known, who, being duly sworn,	to me personally known, who, being duly sworn,
did execute the foregoing affidavit, and did state	did execute the foregoing affidavit, and did state
that he or she was properly authorized by	that he or she was properly authorized by
(Name of Joint Venture)	(Name of Joint Venture)
to execute the affidavit and did so as his or her	to execute the affidavit and did so as his or her
free act and deed.	free act and deed.
Notary Public	Notary Public
Commission expires: (SEAL)	Commission expires: (SEAL)

Date of Issue: March 28, 2024 51 of 70

# SCHEDULE C - Letter of Intent from MBE/WBE (1 of 2) To Perform As Subcontractor, Subconsultant, and/or Material Supplier

Name of Project:		
Project Number:		
FROM:		
(Name of MBE or WBE)	MBE WBE	
TO:		
(Name of Bidder) and Public Build	ding Commission of Chicago	
The undersigned intends to perform work in connection with the	above-referenced project as (check one):	
a Sole Proprietor a Partnership	a Corporation a Joint Venture	
The MBE/WBE status of the undersigned is confirm In addition, in the case whe firm, a Schedule B, Joint Venture Affidavit, is provided.	ned by the attached Letter of Certification, ere the undersigned is a Joint Venture with a non-ME	
The undersigned is prepared to provide the following descrice connection with the above-named project.	ibed services or supply the following described go	oods in
The above-described services or goods are offered for the for Contract Documents.	following price, with terms of payment as stipulated	d in the

# SCHEDULE C - Letter of Intent from MBE/WBE (2 of 2) To Perform As Subcontractor, Subconsultant, and/or Material Supplier

PARTIAL PAY ITEMS For any of the above items that are partial pay items, specifically describe the work and subcontract dollar amount:		
If more space is needed to fully describe tadditional sheet(s).	the MBE/WBE firm's proposed scope of work and/or payment schedule, attack	
SUB-SUBCONTRACTING LEVELS* % of the dollar value of the M	MBE/WBE subcontract will be sublet to non-MBE/WBE contractors.	
% of the dollar value of the M	MBE/WBE subcontract will be sublet to MBE/WBE contractors.	
must be filled in each blank above. If m	sub-subcontracting any of the work described in this Schedule, a zero (0 ore than 10% percent of the value of the MBE/WBE subcontractor's scope and description of the work to be sublet must be provided.	
	to a formal agreement for the above work with the Bidder, conditioned upon it ling Commission of Chicago, and will do so within five (5) working days of receip mission.	
used in the performance of this contract, n policy, codes, state, federal or local laws, n	ne best of its knowledge and belief that it, its principals and any subcontractor neet the Agency requirements and have not violated any City or Sister Agency ules or regulations and have not been subject to any debarment, suspension on agency. Additionally, if at any time the Contractor becomes aware of such the Commission.	
BY:		
Name of MBE/WBE Firm (Print)	Signature	
Date	Name (Print)	
Phone	_	
IF APPLICABLE: BY:		
Joint Venture Partner (Print)	Signature	
Date	 Name (Print) WBE Non-MBE/WBE	
Phone		

Date of Issue: March 28, 2024 53 of 70

# SCHEDULE D - Affidavit of General Contractor Regarding MBE/WBE Participation (1 of 2)

Name of Project:						
STATE OF ILLINOIS	}					
COUNTY OF COOK	<pre>}SS }</pre>					
In connection with the a	n connection with the above-captioned contract, I HEREBY DECLARE AND AFFIRM that I am the					
Title and duly	v authorized representative of					
Name of Ger	neral Contractor whose address is					
and that I have personal in the above-reference	, State of, State of					

Name of MBE/WBE Contractor	Type of Work to be Done in	Dollar Credit Toward MBE/WBE Goals	
	Accordance with Schedule C	MBE	WBE
		\$	\$
		\$	\$
		\$	\$
		\$	\$
		\$	\$
		\$	\$
		\$	\$
		\$	\$
	Total Net MBE/WBE Credit	\$	\$
	Percent of Total Base Bid	%	%

The General Contractor may count toward its MBE/WBE goal a portion of the total dollar value of a contract with a joint venture equal to the percentage of the ownership and control of the MBE/WBE partner.

Date of Issue: March 28, 2024 54 of 70

# SCHEDULE D - Affidavit of General Contractor Regarding MBE/WBE Participation (2 of 2)

\_..

The Undersigned will enter into a formal agreement for the above work with the above-referenced MBE/WBE firms, conditioned upon performance as Contractor of a Contract with the Commission, and will do so within five (5) business days of receipt of a notice of Contract award from the Commission.

Additionally, the Undersigned certifies to the best of its knowledge and belief that it, its principals and any subcontractors used in the performance of this contract, meet the Agency requirements and have not violated any City or Sister Agency policy, codes, state, federal or local laws, rules or regulations and have not been subject to any debarment, suspension or other disciplinary action by any government agency. Additionally, if at any time the Contractor becomes aware of such information, it must immediately disclose it to the Commission.

BY:	
Name of Contractor (Print)	Signature
Date	Name (Print)
Phone	
IF APPLICABLE:	
BY:	
Joint Venture Partner (Print)	Signature
Date	Name (Print)
Phone/FAX	MBE WBE Non-MBE/WBE

# SCHEDULE E - Request for Waiver from MBE/WBE Participation

Date: _						
Public Richard 50 W. V	Ray Giderof, Acting Executive Director Public Building Commission of Chicago Richard J. Daley Center 0 W. Washington Street, Room 200 Chicago, IL 60602					
Dear M	iderof:					
RE:	Contract No.					
	Project Title:					
provision certified the Min	The undersigned certifies that it/we has/have been diligent in our attempt to identify potential subcontractor MBE/WBE to perform work in this project, that such efforts have not been successful, and that it/we cannot mee y/Women Business Enterprise contract goal. These efforts are described below and are consistent with the provisions of the MBE/WBE Program as detailed in Section 23.01.7 as follows:					
Docum	ation attached: yes no					
Based	he information provided above, we request consideration of this waiver request.					
Sincere						
Signatu						
Print N	<u> </u>					
Title						
Name (	rm					

Date of Issue: March 28, 2024 56 of 70

### **Disclosure of Retained Parties**

Pursuant to Resolution No. 5339, as amended by Resolution No. 5371, of the Board of the Public Building Commission of Chicago, the apparent low Bidder is required to submit a fully executed Disclosure of Retained Parties within five (5) days of receipt of notice that it is the apparent low bidder.

### A. Definitions and Disclosure Requirements

- 1. As used herein, "Contractor" means a person or entity that has any contract or lease with the Public Building Commission of Chicago ("Commission").
- 2. Commission contracts and/or qualification submittals must be accompanied by a disclosure statement providing certain information about any lobbyists whom the Contractor has retained or expects to retain with respect to the contract or lease. In particular, the Contractor must disclose the name of each such person, his or her business address, the name of the relationship, and the amount of fees paid or estimated to be paid. The Contractor is not required to disclose employees who are paid solely through the Contractor's regular payroll.
- 3. "Lobbyists" means any person a) who for compensation or on behalf of any person other than himself undertakes to influence any legislative or administrative action, or b) any part of whose duties as an employee of another includes undertaking to influence any legislative or administrative action.

### B. Certification

Cor	actor hereby certifies as follows:	
1.	his Disclosure relates to the following transaction:	-
	. Description of goods or services to be provided under Contract	
		_
2.	lame of Contractor:	_
3.	EACH AND EVERY lobbyist retained or anticipated to be retained by the Contractor with onnection with the contract or lease is listed below. Attach additional pages if necessary.	respect to or in
	Check here if no such persons have been retained or are anticipated to be retained:	_

## Retained Parties:

Name	Business Address	Relationship (Lobbyists, etc.)	Fees (indicate whether paid or estimated)

Date of Issue: March 28, 2024 57 of 70

- 4. The Contractor understands and agrees as follows:
  - a. The information provided herein is a material inducement to the Commission execution of the contract or other action with respect to which this Disclosure of Retained Parties form is being executed, and the Commission may rely on the information provided herein. Furthermore, if the Commission determines that any information provided herein is false, incomplete, or inaccurate, the Commission may terminate the contract or other transaction; terminate the Contractor's participation in the contract or other transactions with the Commission.
  - b. If the Contractor is uncertain whether a disclosure is required, the Contractor must either ask the Commission whether disclosure is required or make the disclosure.
  - c. This Disclosure of Retained Parties form, some or all of the information provided herein, and any attachments may be made available to the public on the Internet, in response to a Freedom of Information Act request, or otherwise. The Contractor waives and releases any possible rights or claims it may have against the Commission in connection with the public release of information contained in the completed Disclosure of Retained Parties form and any attachments.

Under penalty of perjury, I certify that I am authorized to execute this Disclosure of Retained Parties on behalf of the Contractor and that the information disclosed herein is true and complete.

The Contractor also certifies to the best of its knowledge and belief that it, its principals and any subcontractors used in the performance of this contract, meet the Agency requirements and have not violated any City or Sister Agency policy, codes, state, federal or local laws, rules or regulations and have not been subject to any debarment, suspension or other disciplinary action by any government agency. Additionally, if at any time the Contractor becomes aware of such information, it must immediately disclose it to the Commission.

Signature		Date	
Name (Type or Print)		Title	
Subscribed and sworn to before me this day of	, 20	(SEAL)	
Notary Public			
Commission expires:			

Date of Issue: March 28, 2024 58 of 70

# **Performance and Payment Bond**

# BOND NO. SPECIMEN

**Contract No. SPECIMEN** 

KNOW ALL MEN BY THESE PRESENTS, that we	*
with offices in the Principal, an	State of
Illinois as Surety, are held and firmly bound und "Commission", in the penal sum	aws of the State of, with offices in the State of unto the Public Building Commission of Chicago, hereinafter called of Dollars of which sum well and truly to be made, we bind ourselves, our heirs,
executors, administrators, and successors, jointly a	•
•	as the Principal entered into a certain Contract, bereto attached, with the
CPE C	, for the furnishing, fabrication wiven d installation of the

in the referenced projecturea and other miscellaneous work collateral thereto.

NOW, THEREFORE, if the Principal shall well and truly perform and fulfill all the undertakings, covenants, terms, conditions, and agreements of said Contract during the original term of said Contract and any extension thereof that may be granted by the Commission, with or without notice to the Surety, and during the life of any guarantee required under the Contract, and shall also well and truly perform and fulfill all the undertakings, covenants, terms, conditions and agreements of any and all authorized modifications of said Contract that may be made; and also if the Principal shall promptly pay all persons, firms, and corporations supplying labor, materials, facilities, or services in the prosecution of the work provided for in the Contract, and any and all duly authorized modifications of said Contract that may be made, notice of which modifications being hereby waived; and also, if the Principal shall fully secure and protect the said Commission, its legal successor and representative, from all liability in the premises and from all loss or expense of any kind, including all costs of court and attorney's fees, made necessary or arising from the failure, refusal, or neglect of the aforesaid Principal to comply with all the obligations assumed by said Principal or any subcontractors in connection with the performance of said Contract and all such modifications thereof; and also, if the Principal shall deliver all Work called for by said Contract of the Principal with the

Commission, free and clear of any and all claims, liens and expenses of any kind or nature whatsoever, and in accordance with the terms and provisions of said Contract, and any and all modifications of said Contract; then, this said Bond shall become null and void; otherwise it shall remain in full force and effect.

The Surety does further hereby consent and yield to the jurisdiction of the State Civil Courts of the County of Cook, City of Chicago, and State of Illinois, and does hereby formally waive any plea of jurisdiction on account of the residence elsewhere of the Surety. The Principal and Surety severally and jointly agree that this Bond, and the undertakings contained herein, are also for the benefit of any and all subcontractors and other persons furnishing materials, labor, facilities, or services to the Principal or for the performance by the Principal of said Contract with the Commission as figinally executed by said Principal and the Commission or as thereafter modified, and that any experience of the commission of t it subbond a √or\ bersons furnishing labor. mighereth contailed, in the name of the materials, facilities, or services may bring suit on this & d, or a// \unde\ Commission against the said Principal and Suret or her d stood Ιt that this Bond. the e/pred in penal of sum dollars (\$ ), shall secure the payment of all sums due of and by the Principal under the Contract, and guarantee the faithful performance of the Contract.

No modifications, omissions, or additions, in or to the terms of said Contract, the plans or specifications, or in the manner and mode of payment shall in any manner affect the obligations of the Surety in connection with aforesaid Contract. Notice to the Surety of any and all modifications in said Contract of the Principal with the Commission and of any additions or omissions to or from said Contract are hereby expressly waived by the Surety.

		iu nereio
day of 20 the na affixed and these presents duly signed by its undersigned re	presentative pursuant to authority of its governing body	/.
WITNESS:	Y(Seal)	
Name	Individual Principal	
	(Seal)	
Business Address	Individual Principal	
City State	Partner	
CORPORATE SEAL		
	Corporate fincil	
Secretary Title	Title	
Business Advantage		
	Corporate Surety	
BY	Title	
Business Address	CORPORATE SEAL	
The rate of premium of this Bond is \$Total amount of premium charged is \$		

<sup>\*</sup> The current power of attorney for the persons who sign for any surety company shall be attached to this Bond. Such power of attorney shall be sealed and certified with a "first-hand signature" by an officer of the surety. A facsimile signature will not be accepted by the Commission.

<sup>\*\*</sup> Must be filled in by the Corporate Surety.

# **Bond Approval**

BY	
Mary Pat Witry, Secretary Public Building Commission of Chicago	
C	SERTIFICATE AS TO CORPORATE SEAL
I,	in (nd, that who signed on behalf of of said corporation; that I know this person's signature, and the signature was dury signed, sealed, and attested for and in behalf of said corporation by
Dated thisday of	20

CORPORATE SEAL

# **Document Submittal Checklist**

Two originals of the following documents are required at the time of bid opening. Please ensure that you have completed the forms and indicate such by placing an "X" next to each completed item:

1.	 Contractor's Bid (Excel Workbook Bid Form)
2.	 Bid Guarantee (Bond)
3.	 Acceptance of the Bid
4.	 Basis of Award (Award Criteria)
5.	 Schedule of Prices
6.	 Affidavit of Non-Collusion
7.	 Schedule B – Affidavit of Joint Venture (if applicable)
8.	 Schedule C – Letter of Intent from MBE/WBE
9.	 Schedule D – Affidavit of General Contractor Regarding MBE/WBE Participation
10.	 Schedule E – Request for Waiver from MBE/WBE Participation (if applicable)
11.	 Proof of Ability to Provide Payment & Performance Bond
12.	 Proof of Ability to Provide Insurance
13.	 General Contractor's License
14.	 Disclosure of Retained Parties (The apparent low and the apparent 2 <sup>nd</sup> low bidder must submit a fully executed Disclosure of Retained Parties within 5 days after bid opening).

Date of Issue: March 28, 2024 63 of 70

# EXHIBIT #1 COOK COUNTY PREVAILING WAGE RATES – EFFECTIVE MARCH 19, 2024 (Current as of March 28, 2024)

Please	click o	n the l	ink	helow:

https://labor.illinois.gov/content/dam/soi/en/web/idol/laws-rules/conmed/documents/fy24/20240319/Cook.pdf

(Remainder of Page Intentionally Left Blank)

Date of Issue: March 28, 2024 64 of 70

# **EXHIBIT #2 INSURANCE REQUIREMENTS**

# C1607 – CDOT CAPITAL PROGRAM – ALLEYS (Various Locations) PACKAGE 1 CDOT PROJECT #S-3-356

The insurance requirements listed below are the minimum requirements that will be required for work issued on a contract resulting from this Procurement. The actual requirements for the project may be higher and will be determined based on the scope and the requirements as determined in collaboration with the User Agency as determined after award. As noted in this Procurement, Respondent is to submit a certificate of insurance evidencing their current insurance program.

The Contractor must provide and maintain at Contractor's own expense, the minimum insurance coverage and requirements specified below, insuring all operations related to the Contract. The insurance must remain in effect from the date of the Notice to Proceed until Completion of the project, including during completion of Punch List, as well as any time Contractor returns to perform additional work regarding warranties or for any other purpose, unless otherwise noted below or agreed by the Public Building Commission.

# A. INSURANCE TO BE PROVIDED

# 1) Workers' Compensation and Employers Liability (Primary and Umbrella)

Workers' Compensation Insurance as prescribed by applicable law covering all employees who are to provide a service under this Contract and Employers Liability coverage with limits of not less than \$1,000,000 each accident, illness or disease. Coverage will include a waiver of subrogation as required below.

# 2) Commercial General Liability (Primary and Umbrella)

Commercial General Liability Insurance or equivalent with limits of not less than \$2,000,000 per occurrence for bodily injury, personal injury, and property damage liability. Coverage must include the following: All premises and operations, products/completed operations to be maintained for minimum of two (2) years following project completion, explosion, collapse, underground hazards, defense and contractual liability. Contractor and all subcontractors of every tier will specifically name the Public Building Commission of Chicago, the City of Chicago, the City of Chicago Department of Transportation, their respective Board members, employees, elected officials, officers, or representatives, and others as may be required by the Public Building Commission of Chicago, as Additional Insured using the ISO CG2010 0704 and CG2037 0704. Additional Insured status will be on a primary, non-contributory basis for any liability arising directly or indirectly from the work, including the two year completed operations periods. Coverage will include a waiver of subrogation as required below.

Subcontractors performing work for Contractor must maintain limits of not less than \$1,000,000 per occurrence with the same terms herein.

# 3) Automobile Liability (Primary and Umbrella)

When any motor vehicles (owned, non-owned and hired) are used in connection with work to be performed, the Contractor must provide Automobile Liability Insurance, with limits of not less than \$1,000,000 per occurrence for bodily injury and property damage. The Public Building Commission of Chicago, the City of Chicago, the City of Chicago Department of Transportation, their respective Board members, employees, elected officials, officers, or representatives, and others as may be required by the Public Building Commission of Chicago, are to be named as Additional Insured on a primary, non-contributory basis.

Subcontractors performing work for Contractor must maintain limits of not less than \$1,000,000 per occurrence with the same terms herein.

### 4) Contractors Pollution Liability

Contractors Pollution coverage is required with limits of not less than \$2,000,000 per occurrence for any portion of the services, which may entail, exposure to any pollutants, whether in the course of sampling, remedial work or any other

Date of Issue: March 28, 2024 65 of 70

activity under this contract. The contractor pollution liability policy will provide coverage for sums that the insured become legally obligated to pay as loss as a result of claims for bodily injury, property damage and/or clean-up costs caused by any pollution incident arising out of the Work including remediation operations, transportation of pollutants, owned and non-owned disposal sites and any and all other activities of Contractor and its subcontractors. Pollution incidents will include, but not be limited to, the discharge, dispersal, release or escape of any solid, liquid, gaseous or thermal irritant or contaminant, including but not limited smoke, vapors, soot, fumes, acids, alkalis, toxic chemicals, medical waste, waste materials, lead, asbestos, silica, hydrocarbons and microbial matter, including fungi, bacterial or viral matter which reproduces through release of spores or the splitting of cells or other means, including but not limited to, mold, mildew and viruses, whether or not such microbial matter is living.

The policy will be maintained for a period of three years after final completion and include completed operations coverage. The policy will include the Public Building Commission of Chicago, the City of Chicago, Department of Transportation, their respective Board members, employees, elected officials, officers, or representatives, and others as may be required by the Public Building Commission of Chicago, as Additional Insured. These entities must be specifically named and endorsed on the policy. Additional Insured coverage must be on a primary and non-contributory basis for ongoing and completed operations. Coverage will include a waiver of subrogation as required below.

Subcontractors performing work for Contractor must maintain limits of not less than \$1,000,000 per occurrence with the same terms herein. Subcontractors performing environmental work for Contractor must maintain limits of not less than \$1,000,000 per occurrence.

### 5) Professional Liability

When Contractor performs professional work in connection with the Agreement, Professional Liability Insurance must be maintained with limits of not less than \$1,000,000 covering acts, errors, or omissions. The policy will include coverage for wrongful acts, including but not limited to errors, acts or omissions, in the rendering or failure to render professional services resulting in a pollution incident. When policies are renewed or replaced, the policy retroactive date must coincide with, or precede the, start of work on the Agreement. Coverage must be maintained for two years after substantial completion. A claims-made policy, which is not renewed or replaced, must have an extended reporting period of two (2) years.

Subcontractors performing professional work for Contractor must maintain limits of not less than \$1,000,000 per occurrence with the same terms herein.

### 6) Builders Risk/Installation Floater

Contractor must provide All Risk Builders Risk or Installation Floater insurance on a replacement cost basis including but not limited to all labor, materials, supplies, equipment, machinery and fixtures that are or will be permanent part of the facility, inclusive of prior site-work. Coverage must be on an All Risk or Cause of Loss, Special Form basis including, but not limited to, the following: right to partial or complete occupancy, collapse; water damage including overflow, leakage, sewer backup, or seepage; resulting damage from faulty or defective workmanship or materials; resulting damage from error or omission in design, plans or specifications; debris removal; Ordinance and Law and include damage to, false work, fences, temporary structures and equipment stored off site or in transit. The policy will allow for partial or complete occupancy and include damage to existing property at the site.

The Public Building Commission of Chicago, the City of Chicago, the City of Chicago Department of Transportation, their respective Board members, employees, elected officials, officers, or representatives, and any others as may be required by the Public Building Commission will be Named Insureds on the policy. Coverage must be for the full completed value of the work and must remain in place until at least Substantial Completion and may only be cancelled with the written permission of the Public Building Commission, even if the Project has been put to its intended use.

The Contractor is responsible for all loss or damage to personal property including but not limited to materials, equipment, tools, scaffolding and supplies owned, rented, or used by Contractor.

Date of Issue: March 28, 2024 66 of 70

#### B. ADDITIONAL REQUIREMENTS

Contractor must furnish the Public Building Commission Procurement Department, Richard J. Daley Center, Room 200, Chicago, IL 60602, original Certificates of Insurance, or such similar evidence, to be in force on the date of this Contract, and Renewal Certificates of Insurance, or such similar evidence, if any insurance policy has an expiration or renewal date occurring during the term of this Contract. The Contractor must submit evidence of insurance to the Public Building Commission prior to Contract award. The receipt of any certificate does not constitute agreement by the Commission that the insurance requirements in the Contract have been fully met or that the insurance policies indicated on the certificate are in compliance with all Contract requirements. The failure of the Commission to obtain certificates or other insurance evidence from Contractor is not a waiver by the Commission of any requirements for the Contractor to obtain and maintain the specified insurance. The Contractor will advise all insurers of the Contract provisions regarding insurance. Non-conforming insurance does not relieve Contractor of the obligation to provide insurance as specified in this contract. Non-fulfillment of the insurance conditions may constitute a breach of the Contract, and the Commission retains the right to stop work until proper evidence of insurance is provided, or the Contract may be terminated.

The insurance must provide for 30 days prior written notice to be given to the Commission in the event coverage is substantially changed, canceled, or non-renewed.

The Public Building Commission of Chicago reserves the right to obtain copies of insurance policies and records

Any deductibles or self-insured retentions on referenced insurance must be borne by Contractor. All self-insurance, retentions and/or deductibles must conform to these requirements.

The Contractor waives and agrees to cause all their insurers to waive their rights of subrogation against the Public Building Commission of Chicago, the City of Chicago, the City of Chicago Department of Transportation, and any other entity as required by the Public Building Commission of Chicago, their respective Board members, employees, elected officials, officers, or representatives. The Contractor must require each Subcontractor to include similar waivers of subrogation in favor of the Commission, the City of Chicago, the City of Chicago Department of Transportation, and any other entity as required by the Public Building Commission of Chicago.

The insurance coverage and limits furnished by Contractor in no way limit the Contractor's liabilities and responsibilities specified within the Contract or by law.

Any insurance or self-insurance programs maintained by the Public Building Commission of Chicago, the City of Chicago, the City of Chicago Department of Transportation, and any other entity as required by the Public Building Commission of Chicago, will not contribute with insurance provided by the Contractor under the Contract.

The required insurance to be carried is not limited by any limitations expressed in the indemnification language in this Contract or any limitation placed on the indemnity in this Contract given as a matter of law.

If contractor is a joint venture or limited liability company, the insurance policies must name the joint venture or limited liability company as a Named Insured.

The Contractor must require all subcontractors to provide the insurance required herein, or Contractor may provide the insurance for subcontractors. All subcontractors are subject to the same insurance requirements of Contractor unless otherwise specified in this Contract.

If Contractor or subcontractor desires additional coverage, the party desiring the additional coverage is responsible for the acquisition and cost.

Date of Issue: March 28, 2024 67 of 70

Contractor must submit the following at the time of award:


- 1. Standard ACORD form Certificate of Insurance issued to the Public Building Commission of Chicago as Certificate Holder including:
  - a. All required entities as Additional Insured
  - b. Evidence of waivers of subrogation
  - c. Evidence of primary and non-contributory status
- 2. All required endorsements including the CG2010 and CG2037

The Public Building Commission reserves the right to modify, delete, alter or change these requirements.

REMAINDER OF PAGE LEFT BLANK INTENTIONALLY

Date of Issue: March 28, 2024 68 of 70

# **EXHIBIT #3 PROJECT COMMUNITY AREA MAP**

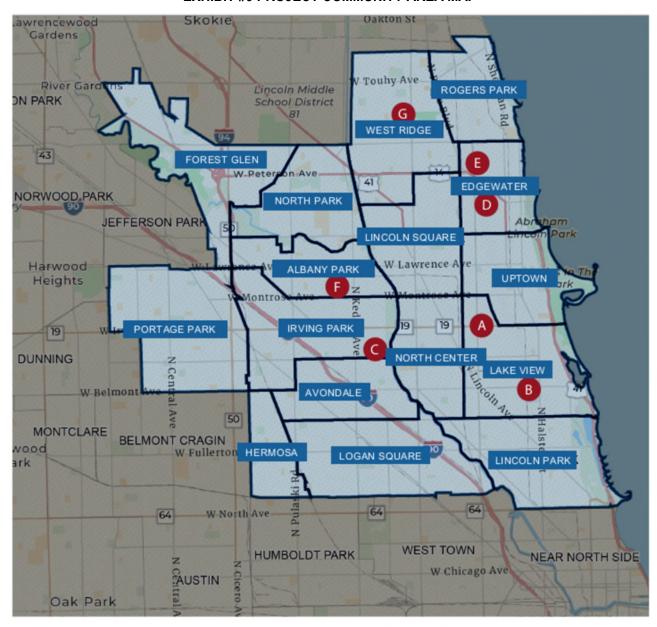

# **CDOT Neighborhood Improvment Alleys**

- Project location
- A Belle Plaine E Glenlake/Paulina
- B Roscoe/Clark F Wilson/ Sunnyside
- Waveland/Troy
   G North Shore/Artesian
- D Hollywood/Hermitage
- Community Areas



Date of Issue: March 28, 2024 69 of 70

#### **EXHIBIT #4 ASSIST AGENCIES**

# PUBLIC BUILDING COMMISSION OF CHICAGO'S ASSIST AGENCIES

Assist Agencies are Chambers of Commerce and Not-for-Profit agencies that represent the interests of small, minority- and/or women-owned businesses. For the most up-to-date contact information, visit <a href="mailto:pbcchicago.com/doing-business/assist-agencies/">pbcchicago.com/doing-business/assist-agencies/</a>

#### **African American Contractors Association**

PO Box #19670 Chicago, IL 60619 Omar Shareef 312-915-5960 aacanatlassoc@gmail.com www.aacanatl.org

#### Chatham Business Association: Small Business Development, Inc.

800 E 78th St Chicago, IL 60619 Melinda Kelly (773) 994-5006 melindakelly@cbaworks.org cbaworks.org

### Chicago Urban League

4510 S Michigan Ave, 3rd Floor Chicago, IL 60653 Kelly Evans (773) 451-3547 kevans@chiul.org chiul.org

#### Construction Business Development Center at Prairie State College

202 S Halsted St Chicago Heights, IL 60411 Cathy Svetanoff (708) 709-3568 csvetanoff@prairiestate.edu prairiestate.edu

# Hispanic American Construction Industry Association

650 W Lake St, #415 Chicago, IL 60661 Ivette Trevino (312) 575-0389 itrevino@haciaworks.org haciaworks.org

#### South Shore Chamber, Inc.

1750 E 71st St Chicago, IL 60649 Tonya Trice (773) 955-9508 ttrice@southshorechamberinc.org southshorechamberinc.org

# Women's Business Development Center

8 S Michigan Ave, #400 Chicago, IL 60603 Donna Beasley (312) 853-3477 dbeasley@wbdc.org wbdc.org

Last Updated: 10/2/2023 12:11 PM

#### **Black Contractors United**

12000 S Marshfield Ave Calumet Park, IL 60827 Carole Williams 708-389-5730 bcunewera@att.net blackcontractorsunited.com

### Chicago Cook Workforce Partnership 69 W Washington Street

Suite 2860 Chicago, IL 60602 Marissa Lewis mlewis@chicookworks.org (312) 603-0200 chicookworks.org

# Chicago Women in Trades

2444 W 16th St Chicago, IL 60608 Jayne Vellinga (312) 942-1444 jvellinga@cwit2.org chicagowomenintrades2.org

#### **Federation of Women Contractors**

4210 W Irving Park Rd Chicago, IL 60641 Jaemie Neely (312) 360-1122 info@fwcchicago.com fwcchicago.com

### Illinois Black Chamber of Commerce

411 Hamilton Blvd, #1404 Peoria, IL 61602 Larry Ivory & Kenyatta Fisher (309) 740-4430 Iarryivory@illinoisblackchamber.org, kfisher@ilbcc.org illinoisblackchamber.org



# **CANDO** Corporation

1633 S Michigan Ave Chicago, IL 60615 LaVerne Hall (312) 488-9338 LHall@candocorp.net

#### Chicago Minority Supplier Development Council

216 W Jackson Boulevard Suite 600 Chicago, IL 60606 Debra Jennings-Johnson (312) 755-8880 info@ChicagoMSDC.org chicagomsdc.org

#### ConstructConnect

3825 Edwards Road, #800 Cincinnati, OH 45209 Amanda Beyer (513) 458-5837, Extension 5108336 amanda.beyer@constructconnect.com ConstructConnect.com

#### HIRE360 Chicago

2301 S Lake Shore Drive Lakeside Center, Chicago, IL 60616 Deborah Whitaker (312) 575-2500 dwhitaker@hire360chicago.com bids@hire360chicago.com

# Rainbow/PUSH Coalition 930 E 50th St

930 E 50th St Chicago, IL 60615 John Mitchell (773) 256-2766 jmitchell@rainbowpush.org rainbowpush.org

## **U.S. Minority Contractors Association**

1250 Grove Ave, #200
Barrington, IL 60010
Larry Bullock
(847) 852-5010
larry.bullock@usminoritycontractors.org
usminoritycontractors.org

# **Women Construction Owners & Executives**

308 Circle Ave Forest Park, IL 60130 Mary Kay Monaghan (708) 366-1250 mkm@mkmservices.com wcoeusa.org

Date of Issue: March 28, 2024 70 of 70
